

Akron
Engineering
Bureau

2007 Annual Report



**City of Akron
Department
of Public Service**

Donald L. Plusquellic
Mayor

Gerald Holland
Service Director

David J. Celik, P.E.
City Engineer

Akron Engineering
Bureau
166 South High Street
Akron, Ohio
44308-1652
(330) 375-2355
Fax (330) 375-2288
AkronEngineering@
ci.akron.oh.us



Appendix

AEB Vision and 2007 Goals
2007 Major Accomplishments
Final Goals Status Report
Organization Chart
Status of Permanent Personnel
Operating Budget Chart
Applied Overhead Chart
Direct Overhead Chart

Billable Time vs. Overhead
CIP Revenues & Expenditures
Construction Contract Data
Bridge Inspection Summary
Street Improvement Petitions
Mapping Requests
PROJECT REPORTS



AEB Vision

Our vision is to provide professional engineering services that meet the infrastructure needs of our customers by:

Planning projects that meet the goals of the City.

Designing projects in a cost effective manner.

Constructing projects in compliance with the contract documents.

To reach this vision means:

Utilizing the experience, education and training of our employees to create a more flexible work force.

Empowering our employees to manage projects more independently.

Use of innovative plan development, design and construction techniques to minimize project costs.

Maintaining the highest level of ethics and professionalism.

Long Term Vision Affirmation

We will affirm and re-enforce our vision by operating the AEB with the following philosophy:

Reduce the need for supervision by creating additional Engineering Technician III and Civil Engineer III promotional opportunities, and filling those positions with capable and motivated employees who can independently coordinate all aspects of a project.

Assign employees based on:

The overall needs of the AEB.

The experience level necessary to administer the specific project.

The opportunity to diversify the experience of the workforce.

The expectation of minimizing project costs.

Rotate employees between the Design/Environmental Division and the Construction Division so that all employees become proficient in both project design and construction administration.

Maintain the proper balance between in-house design and consultant design.

Determine and monitor overhead rates including project development and programming costs in order to fully understand the cost-effectiveness of the AEB.

Akron Engineering Bureau
Department of Public Service
2007 Goals 4th Quarter Update

2007 Goals	2007 Status to Date
Bureau-Wide Goals	
<p>Establish a better flow of feedback from Construction following project completion. The current project evaluation form often times does not get completed for several months after construction is complete. After that much time as elapsed, any issues encountered in the field are no longer fresh in the mind of the RPR and the result is a project evaluation that has very little detail.</p> <p>This goal is in line with the Internal Business Process Section of the Engineering Bureau Balanced Scorecard.</p>	<p>Project evaluation forms are being completed at sub-final stage in order to reduce the time gap. This was initiated in June, 2007.</p>
Administrative Services	
<p>Update and better organize the information on the Engineering web page by the end of March 2007.</p> <p>This goal is in line with the Customer Service Section of the Engineering Bureau Balanced Scorecard.</p>	<p>The updates were identified in August. The new page format is being designed. New software to allow completion was received. Goal was put on hold when the administration announced a plan to develop a citywide web page.</p>
<p>Investigate ways to make the Construction Division filing task more efficient. Implement those ways that are found to be feasible.</p> <p>This goal is in line with the Internal Business Process Section of the Engineering Bureau Balanced Scorecard.</p>	<p>The Document Management System Project started up in December, 2006. This project will dramatically change the record-keeping function of the Engineering Bureau. The project was put on hold March 12, 2007. No changes will be made until a decision about the Document Management System Project is made. .</p>

<p>Review 57 boxes of as-built drawings to determine if the information has been captured on the record drawings and on the underground record. Obsolete prints will be disposed.</p> <p>This goal is in line with the Internal Business Process Section of the Engineering Bureau Balanced Scorecard.</p>	<p>This goal was completed by the end of January, 2007.</p>
Design Division	
<p>Update the Construction and Material Specifications book for use beginning with the 2008 construction season.</p> <p>This goal is in line with the Learning and Growth Section of the Design Division Scorecard.</p>	<p>Most of the updates have been completed, and a draft version has been placed on the S: Drive for City-wide review. Impacted standard drawings brought about the spec book changes that have been identified. Publication of the new book and updates to the standard drawings should be completed by the beginning of the 2008 construction season.</p>
<p>Develop an Underground Utility Relocation design manual.</p> <p>This goal is in line with the Learning and Growth Section of the Design Division Scorecard.</p>	<p>A preliminary section of the manual has been drafted. Progress is on hold while the strategy for underground utility relocation is under review.</p>
<p>Provide additional training on the new EPA Phase 2 Rules that deal with the post construction best management practices.</p> <p>This goal is in line with the Learning and Growth Section of the Design Division Scorecard.</p>	<p>Training session held on February 1 to present the Draft BMP Guidance Document to staff members.</p>

Environmental Division	
<p>Research and identify ODNR, EPA, and other state and federal agency grant programs available for funding Environmental Division projects and compile fact sheets and information about the programs for distribution by <u>June 1, 2007</u>. Review CIP requests to identify grant funding possibilities by <u>October 1, 2007</u>.</p> <p>This goal is in line with the Financial Section of the Environmental Division Scorecard.</p>	<p>Applications were completed and submitted for HUD-EPA appropriations and Water Resource Development Act (WRDA) in first quarter of 2007.</p> <p>Also potential new legislation is being reviewed for Brownfield Application (Good Samaritan Law).</p> <p>The Energy Efficiency Block Grant Program (HR 3236) will be tracked as it moves through Congress in 2007. Potential program involvement will be coordinated with Paula Davis, KAB.</p> <p>Grants available through agencies such as ODNR, FEMA, and ODOD have been researched and a draft list of funding opportunities and program information has been compiled. This information will be further reviewed and edited, and condensed into the fact sheets in 4th quarter.</p>
<p>Conduct a project Management Seminar (with the Design Division) prior to <u>April 1, 2007</u>. The goals of the seminar are to review:</p> <ul style="list-style-type: none"> • Current procedures for in house as well as consultant projects. • When and how to use a supplemental services consultant. • Doing a project cradle to grave • How to lock a scope to prevent creep • Dealing with outside agencies, ODOT, EPA, Corps of Engineers, etc. • Paper and electronic trails <p>This goal is in line with the Learning and Growth and Internal Business Process Section of the Environmental Division Scorecard.</p>	<p>The Project Management Seminar was held on March 28, 2007. The final topics included:</p> <p>Review of goals for 2007 Project Management Procedures Project Schedules Consultant Contracts Underground Records Paper Trails / Standard Forms Quality Based Selection Project Evaluations Storm Water NPDES Requirements</p>

<p>Compile information from the AEB Consultant Performance Review (includes both Design Divisions of AEB) forms to create an “AEB resume” for the Consultants that lists recent projects, the ratings for the project, and the Consultant and AEB Project Managers that worked on the project prior to <u>September 1, 2007</u>. Make this information available on the server so that it can be used as a tool when making consultant selections.</p> <p>This goal is in line with the Internal Business Process Section of the Environmental Division Scorecard.</p>	<p>The consultant evaluation forms are currently scanned and made available on the AEB server.</p> <p>The format of the summary document is still being discussed and will be finalized in the 3rd quarter (fully implemented in the 4th quarter).</p> <p>Consultant Evaluation Forms that are available on the server have been reviewed and information to be listed in the performance report has been identified. The report format still needs to be finalized. The program to be used (Excel or Access) will be determined and the information currently available will be input in the 4th quarter.</p>
<p>Implement a City GIS layer for City of Akron Bridges prior to <u>December 1, 2007</u>. Develop a format and data list in the first quarter, prior to <u>April 1, 2007</u>, for full implementation by the end of the year. Development of this layer should consider the future potential of the use of a computerized (notepad/arcpad) data collection for conducting field inspections</p> <p>This goal is in line with the Internal Business Process Section of the Environmental Division Scorecard.</p>	<p>GIS training of staff completed in first quarter.</p> <p>The administration has requested a mowing layer which will incorporate all areas now mowed by Parks, APUB, Customer Service, and Planning. Our goal is to complete this layer before the end of 2007.</p> <p>Bridge layer has been completed.</p>

Construction Division	
<p>Update the Resident Project Representative Source Book by March 31, 2007.</p> <p>This goal is in line with the Learning and Growth Section of the Construction Division Scorecard.</p>	<p>The RPR Source Book was reviewed and no updates were necessary this year.</p>
<p>Conduct the Resident Project Representative seminar by March 31, 2007.</p> <p>This goal is in line with the Learning and Growth Section of the Construction Division Scorecard.</p>	<p>The RPR Seminar was held on March 21, 2007.</p>
<p>Continue to monitor Gypsy Moth infestation and work with the Ohio Department of Agriculture to have the highest levels treated by June 15, 2007.</p> <p>This goal is in line with the Customer Service Section of the Engineering Bureau Balanced Scorecard</p>	<p>Gypsy Moth levels this year do not warrant treatment.</p>
<p>Develop a long-range management strategy for the Emerald Ash Borer infestation by June 15, 2007.</p> <p>This goal is in line with the Customer Service Section of the Engineering Bureau Balanced Scorecard</p>	<p>The plan has been completed and will be submitted to the Planning Department for funding in the 2008 Capital Improvement Program.</p>
<p>Bid and complete the White Pond Drive Gateway planting by September 30, 2007, pending approval of the beautification grants from ODOT.</p> <p>This goal is in line with the Customer Service Section of the Engineering Bureau Balanced Scorecard</p>	<p>ODOT has not awarded the grants.</p>

DESIGN DIVISION

ACTING MANAGER:

Dave Wilkerson, P.E.
330-375-2217

Bob Geiser, P.E., Civil Engineer III – 375-2162
Beth Mettle, Applications Analyst – 375-2528 ext 3140
Rob Scarlatelli, P.E., Civil Engineer III – 375-2788

Michelle DiFiore, P.E., Senior Engineer – 375-2495

Chris Jonke, P.E., Civil Engineer III – 375-2015
Dennis Hawthorne, Engineering Tech. II – 375-2528 ext 6467

Bill Marras, AIA, Engineering Projects Coordinator – 375-2163
Wayne Bachus, Engineering Technician III – 375-2528 ext 3126
Sanford Taylor, Architectural Designer II – 375-2383

Mike Teodecki, P.E., Senior Engineer – 375-2336
Jim Hall, Civil Engineer II – 375-2339
Randy Keirns, P.E., Civil Engineer III – 375-2167
Dianne Reed, Engineering Technician II – 375-2528 ext 3130
Chad Root, P.E., Civil Engineer III – 375-2483

Dave Wilkerson, P.E., Senior Engineer – 375-2217
Rick Fischer, Engineering Technician III – 375-2528 ext 3339
Alicia Garnett, Drafter II – 375-2528 x3134
Phil Rohr, P.E., Civil Engineer II – 375-2265

SURVEY SECTION

Mike Hudik, P.S., Survey Projects Supervisor – 375-2375
Jim Vechery, Surveyor Aide III – 375-2282

FAX 330-375-2353

City Engineer

PHONE 330-375-2095
FAX 330-375-2574

CONSTRUCTION DIVISION

MANAGER:

James P. Weber, P.E.
330-375-2740

SENIOR ENGINEER:

Mark J. Moore, P.E.
330-375-2496

CIVIL ENGINEER III

Travis Capper, P.E.
330-375-2699

Jim Anderson, Engineering Tech. III – 375-2528 ext 3466
JuanPablo Ascarrunz, Engineering Tech. III – 375-2521
Mike Brehob, Engineering Projects Coordinator – 375-2394
Dave Cooke, Engineering Projects Coordinator – 375-2097
Karen Dyer, Engineering Projects Coordinator – 375-2104
Rick Falkenstein, Engineering Technician III – 375-2740
Fred Fassnacht, Engineering Technician III – 375-2740
Bill Hahn, City Arborist & Horticulturist – 375-2373
Mike Huber, Materials Lab Supervisor – 375-2861
Chad Kobelt, Engineering Technician II – 375-2528
Jon Malish, Landscape Technician II – 375-2731
Paul McCutcheon, Engineering Technician III – 375-2740
Corey Moke, Engineering Technician II – 375-2740
Larry Peaslee, Engineering Technician III – 375-2740
Barry Pruitt, Engineering Technician II – 375-2528
Adam Staller, Engineering Technician II – 375-2381
Bill Stump, Engineering Technician II – 375-2521
David Wright, Engineering Tech. II – 375-2528 ext 3134
Mike Wytryszczewski, Engr. Projects Coord. – 375-2190
Jason Zajac, Engineering Technician II – 375-2740

FAX 330-375-2344

ENVIRONMENTAL DIVISION

MANAGER:

Patrick D. Gsellman, P.E.
330-375-2357

SENIOR ENGINEER:

Bradford A. Beckert, P.E.
330-375-2382

Scott Davenport, Engineering Technician III – 375-2769
Andy Davis, P.E., Civil Engineer III – 375-2377
Genny Hanna, P.E., Civil Engineer III – 375-2494
Mark Pirie, Engineering Technician III – 375-2492
Jeff VanNatten, Drafter III – 375-2528 ext 3468

FAX 330-375-2517

ADMINISTRATIVE SERVICES


MANAGER:

Kenneth F. Kostura, P.E.
330-375-2355

Larry Thomas, Engineering Technician III
330-375-2374

Beverly Carlson, Secretary III – 375-2528 x6028
Wendy Doyle, Cartographer – 375-2528 ext 6029
Linda Fallon, Account Clerk III – 375-2528 ext 4876
Brent Kelley, Engineering Technician II – 375-2491
Charles Hirsch, Engineering Tech. II – 375-2528 x6066
Marianne Kracker, Secretary II – 375-2355
Michele Mann, Secretary III – 375-2528 x3310

FAX 330-375-2288

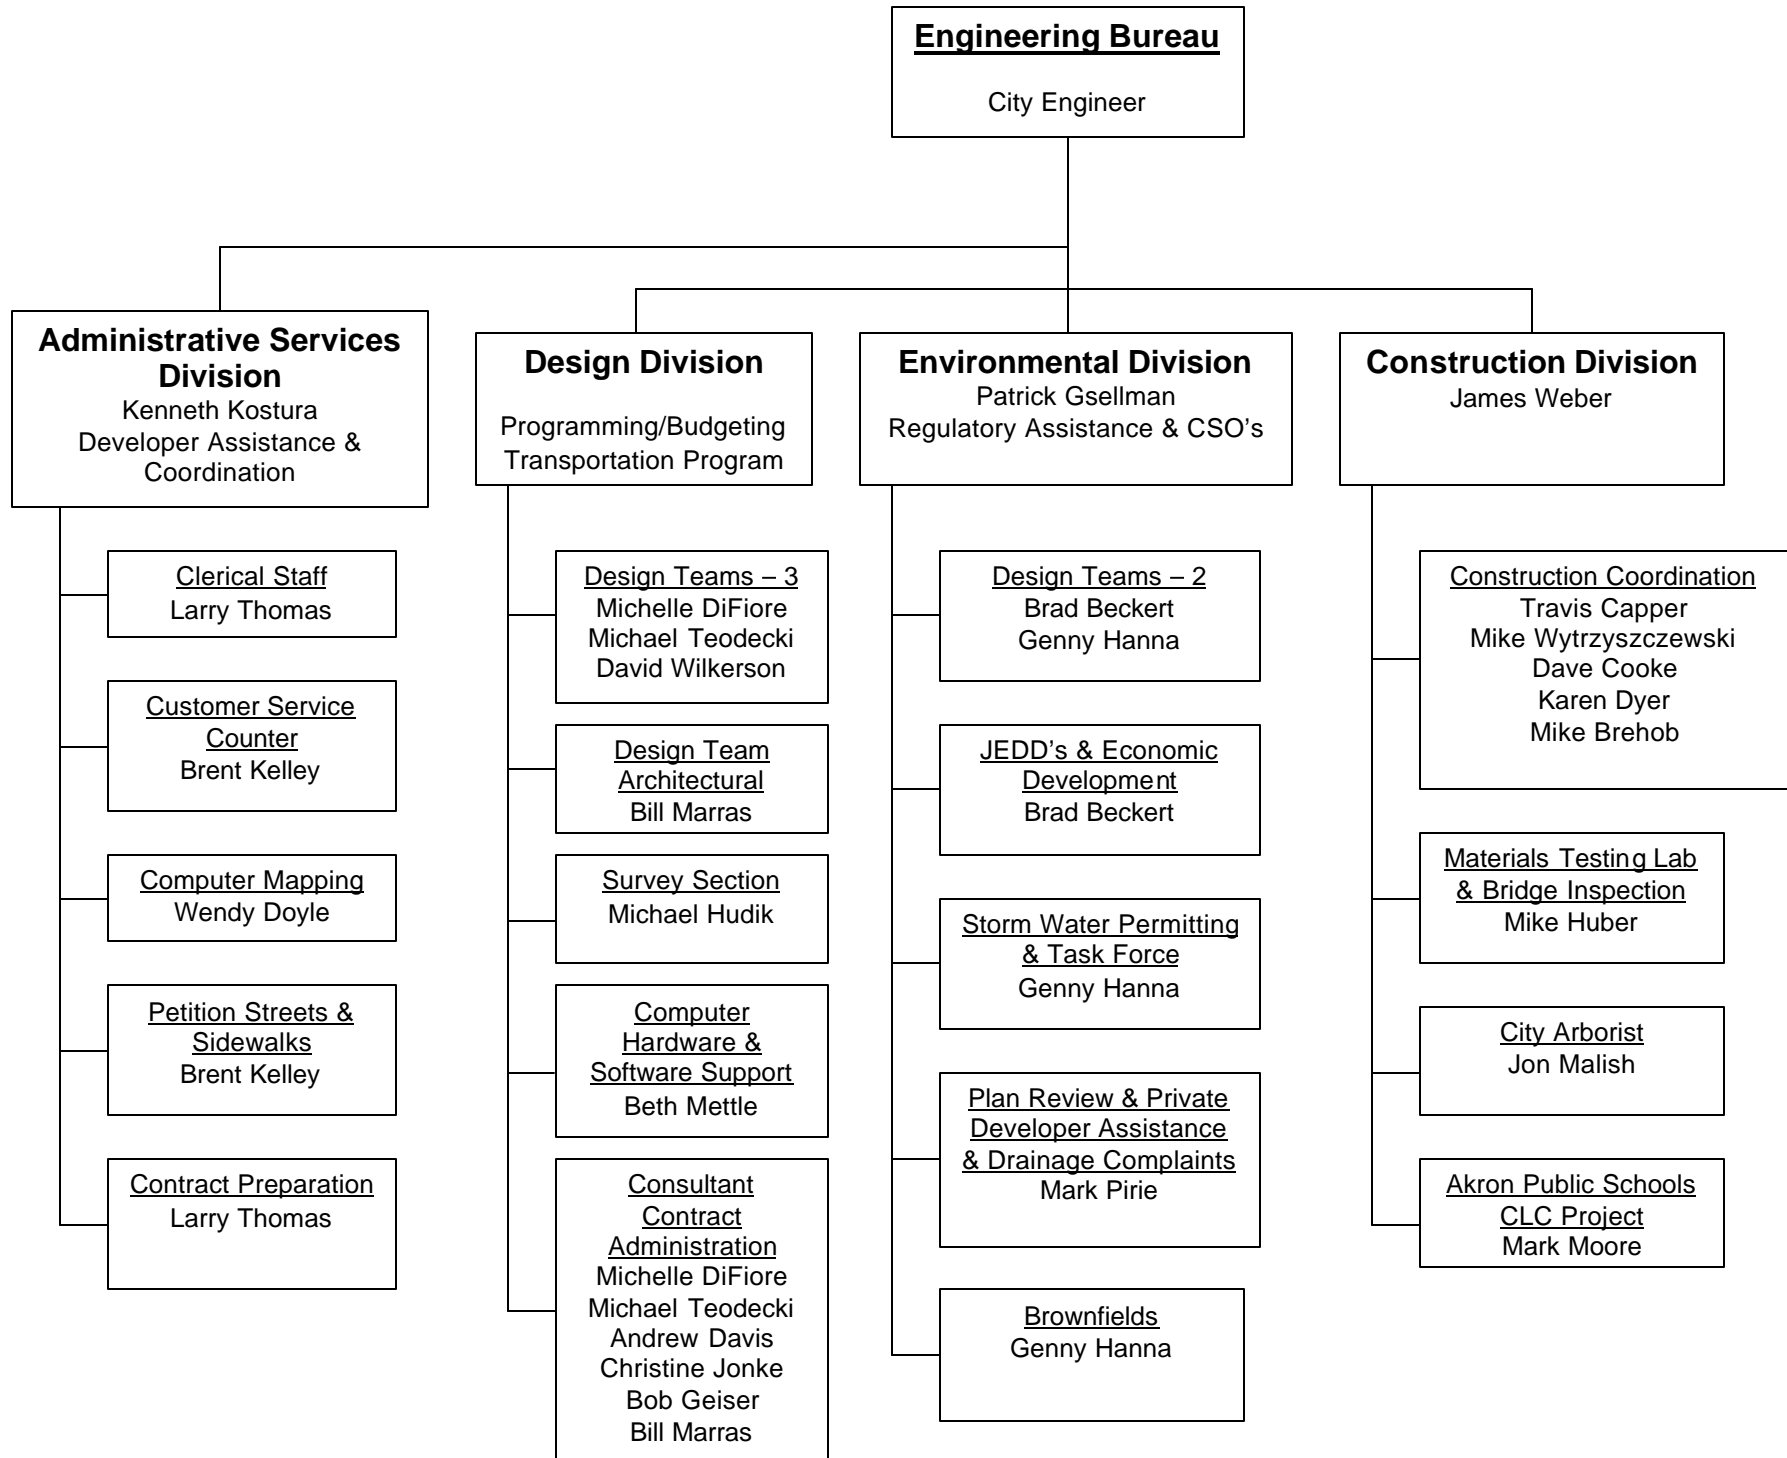

**STATUS OF PERMANENT ENGINEERING BUREAU PERSONNEL
AS OF JANUARY 1, 2008**

CLASSIFICATION/NAME	CHANGE IN STATUS
<u>CITY ENGINEER</u> DAVID J. CELIK	Retired 12/1/07
<u>ENGINEERING DIVISION MANAGERS</u> PATRICK D. GSELLMAN KENNETH F. KOSTURA MICHAEL L. MADONIO JAMES P. WEBER	
<u>SENIOR ENGINEER</u> BRADFORD A. BECKERT TRAVIS L. CAPPER MICHELLE DIFIORE EUGENIE HANNA MARK J. MOORE MICHAEL J. TEODECKI DAVID C. WILKERSON	Promoted 10/29/07 Promoted 4/2/07
<u>CIVIL ENGINEER III</u> ANDREW J. DAVIS ROBERT GEISER TISH JERNIGAN CHRISTINE JONKE RANDALL KEIRNS CHAD ROOT ROB SCARLATELLI	Promoted 6/11/07
<u>CIVIL ENGINEER II</u> JAMES L. HALL PHILIP A. ROHR <u>CIVIL ENGINEER I</u> AARON J. SMITH	Resigned 11/27/07

<u>ENGINEERING PROJECTS</u> <u>COORDINATOR</u> MICHAEL BREHOB DAVID S. COOKE KAREN B. DYER WILLIAM J. MARRAS MICHAEL D. WYTRZYSZCZEWSKI	
<u>CITY ARBORIST & HORTICULTURIST</u> BILL HAHN	Retired 2/1/07
<u>LANDSCAPE TECHNICIAN II</u> JONATHAN MALISH	
<u>CONSTRUCTION MATERIALS</u> <u>LABORATORY SUPERVISOR</u> MICHAEL D. HUBER	
<u>ENGINEERING TECHNICIAN III</u> JAMES M. ANDERSON JUANPABLO ASCARRUNZ WAYNE BACHUS T. SCOTT DAVENPORT RICHARD J. FALKENSTEIN FREDERICK J. FASSNACHT RICHARD W. FISCHER JASON HARRIS PAUL A. McCUTCHEON LARRY D. PEASLEE MARK S. PIRIE LARRY F. THOMAS	

<u>ENGINEERING TECHNICIAN II</u> DENNIS L. HAWTHORNE CHARLES HIRSCH K. BRENT KELLEY CHAD KOBELT COREY MOKE BARRY PRUITT DIANNE R. REED ADAM STALLER WILLIAM STUMP DAVID WRIGHT JASON ZAJAC	
<u>ENGINEERING TECHNICIAN I</u>	
<u>SURVEYING PROJECT SUPERVISOR</u> MICHAEL J. HUDIK	
<u>SURVEYOR</u> JEFFREY CASTON DONALD VARDON	
<u>SURVEYOR AIDE III</u>	
<u>SURVEY PARTY CHIEF</u> JAMES P. VECHERY	Promoted 11/5/07
PHILIP W. VUKODER	Resigned 5/4/07
<u>ARCHITECTURAL DESIGNER II</u> SANFORD TAYLOR	
<u>CARTOGRAPHER</u> WENDY DOYLE	
<u>APPLICATIONS ANALYST</u> BETH METTLE	
<u>SECRETARY III</u> BEVERLY CARLSON MICHELE MANN	
<u>SECRETARY II</u> MARIANNE KRACKER	

<u>ACCOUNT CLERK III</u> LINDA S. FALLON	
<u>DRAFTER II</u> ALICIA GARNETT	Promoted 2/26/07
<u>DRAFTER III</u> JEFFREY VANNATTEN	


O:\Drive\administrative files\non-project correspondence\admin services misc\2006 status of bureau personnel.doc



2007 Engineering Operating Budget

Labor	\$4,063,421.75
Fringe Benefits	\$1,651,960.81
Direct Expenditures	\$114,760.73
Utilities	\$23,730.67
Debt Service	\$20,967.67
Insurance	\$14,000.00
Rentals & Leases	\$0.00
Capital Outlay	\$0.00
Interfund Charges	<u>\$494,837.23</u>
Grand Total	\$6,383,678.86


2007 Engineering Operating Budget

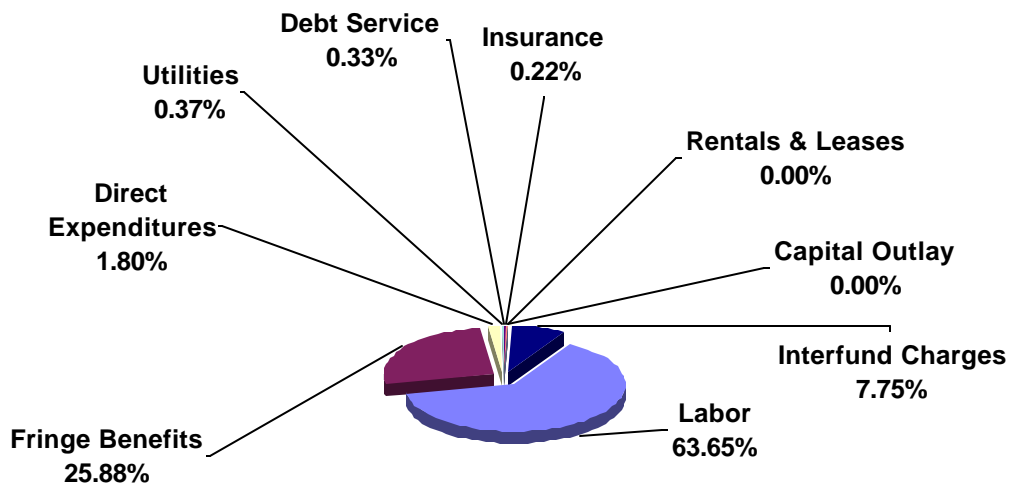



2007 Applied Overhead


Management Salaries	\$474,520.47
Office Support Salaries	\$328,608.40
Management and Office Support Benefits	\$556,648.61
Bridge Inspection	\$21,862.00
Non-Project Studies & Reports	\$77,010.00
Technical Assistance	\$75,930.00
Underground Records & Mapping	\$25,157.00
Developer Assistance	\$17,249.00
Training	\$79,216.00
World Class Organization	\$301.00
Direct Expenditures	\$114,760.73
Utilities	\$23,730.67
Debt Service	\$20,967.67
Insurance	\$14,000.00
Rentals & Leases	\$0.00
Capital Outlay	\$0.00
Interfund Charges	\$494,837.23
Grand Total	\$2,324,798.78

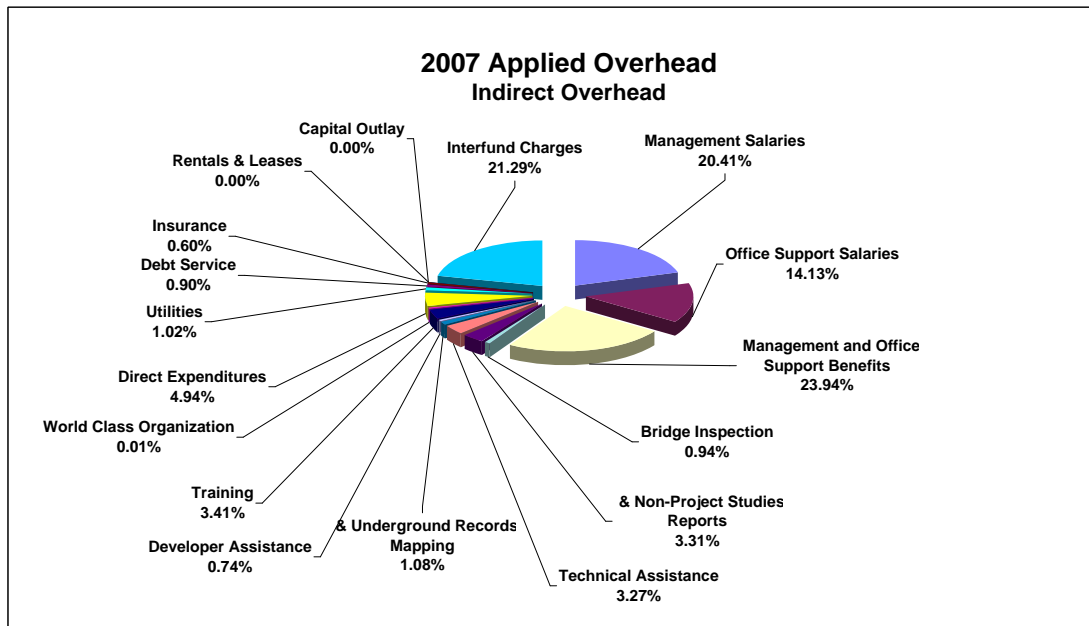



2007 Direct Overhead


Health Benefits	\$710,400.00
Worker's Compensation	\$116,242.46
Unemployment Compensation	\$0.00
Medicare Insurance	\$40,097.83
PERS - City Share	\$577,078.55
Retirement Payout	\$208,141.97
Longevity Pay	\$49,999.35
Leave Purchase	\$38,171.20
Uniform Allowance	\$2,275.00
Sick Leave	\$94,255.59
Holiday Pay	\$153,500.79
Annual Leave	\$298,506.14
Compensatory Time Off	<u>\$12,027.00</u>
Grand Total less Management and Office Support Benefits @ \$556,648.61	\$1,744,047.27

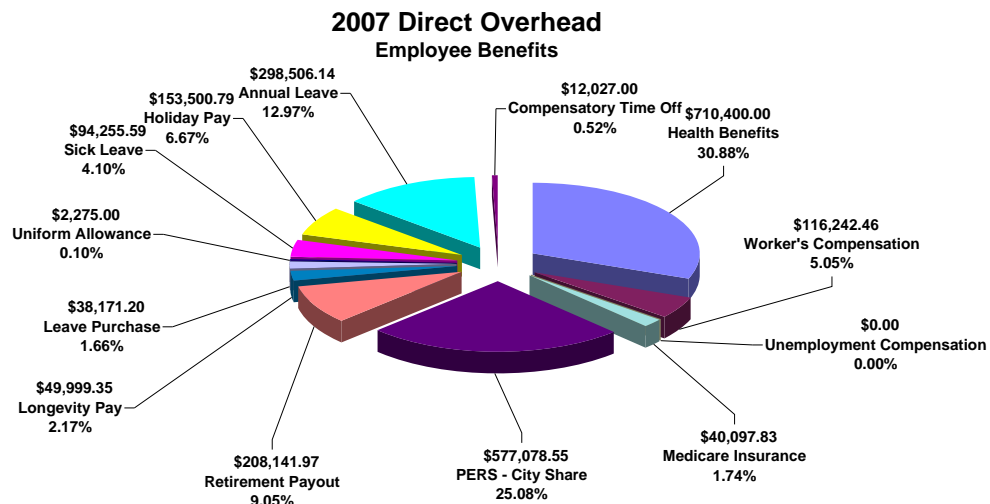



2007 Billable Time vs Overhead Comparisons

Billable Time	\$1,941,949.61
Direct Overhead (Employee Benefits)	\$1,744,047.27
Indirect Overhead	<u>\$2,324,798.78</u>
	\$6,010,795.66

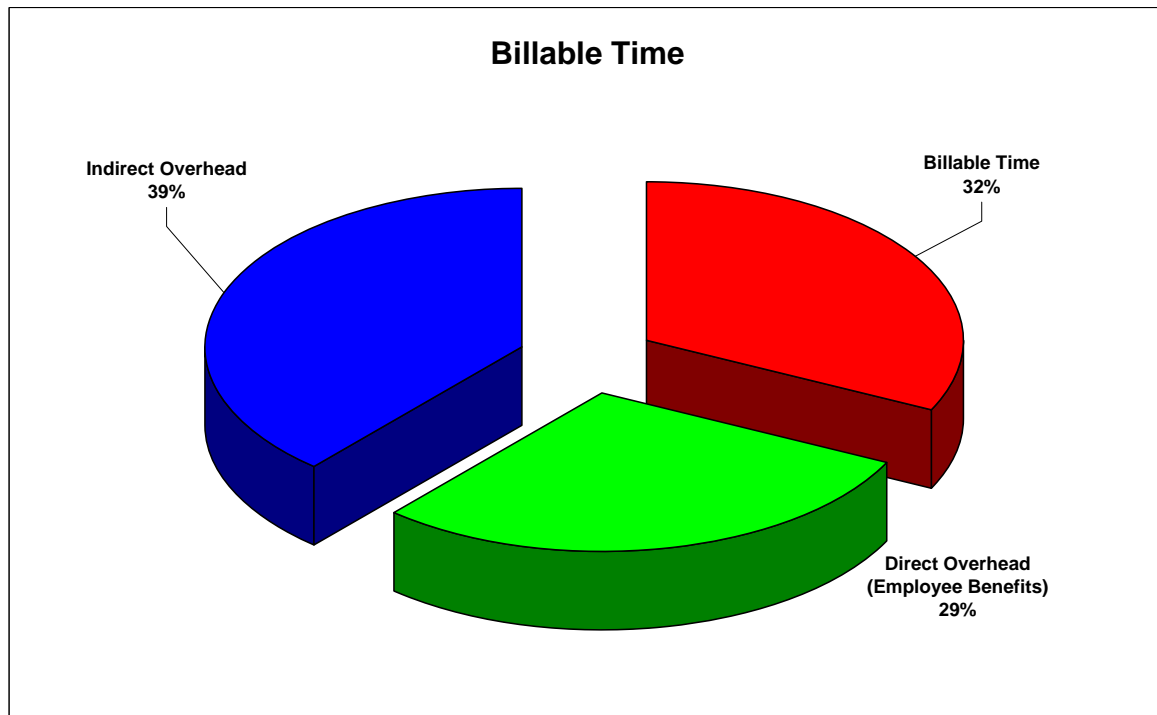



2007 CAPITAL INVESTMENT & COMMUNITY DEVELOPMENT PROGRAM REVENUE & EXPENDITURE SUMMARY

For the year 2007, City Council approved a \$189,616,000 Capital Investment and Community Development Program. The funding comes from a number of federal, state and local funding sources as shown in the following chart. The program consists of several categories of projects, including Federal & State Transportation projects. The program also includes the housing and human resources program, debt service, preliminary engineering and closeouts, and program overhead costs in addition to the construction projects.


2007 Sources of Revenue

Income Tax	\$35,007,000
General Obligation Debt	\$38,170,000
Sewer Capital Fund	\$10,636,000
Water Capital Fund	\$6,875,000
Community Development	\$9,785,000
Federal & State Transportation Funds	\$21,325,000
Ohio Public Works Commission Funds	\$11,627,000
Other	\$56,191,000
Grand Total	\$189,616,000


2007 Program Expenditures

Public Utilities	\$25,693,000
Transportation	\$62,008,000
Economic Development	\$39,984,000
Debt Service	\$28,816,000
Housing & Human Resources	\$7,020,000
Public Facilities	\$9,118,000
Parks & Recreation	\$10,227,000
Other	\$6,750,000
Grand Total	\$189,616,000

2007 Sources of Revenue

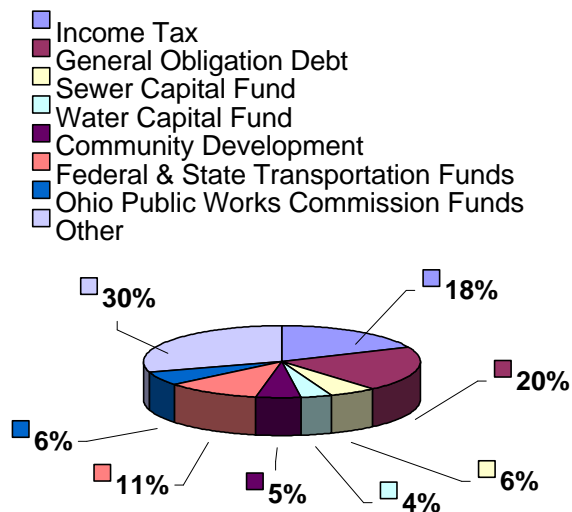

2007 Program Expenditures

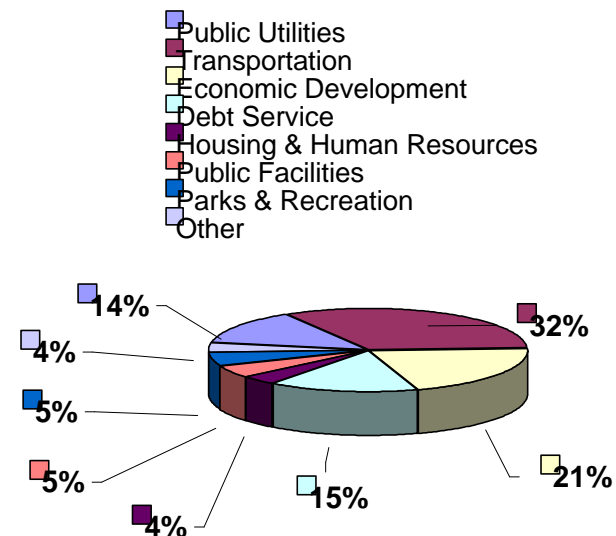

2007 Awarded Construction Contracts

Project Name	Contractor	Bid Date	Award Date	Construction Amount
Main Street Building Renovation	Cardinal Environmental Service Co.	12/7/2006	1/2/2007	\$468,330.00
Sanitary Sewer Reconstruction 2005 RECORD	Cioffi & Son Construction Co.	12/12/2006	1/2/2007	\$351,879.25
Balch Auditorium Improvements Record Drawing	Tri-Master Inc.	12/13/2006	1/22/2007	\$125,535.00
Elm Drive Wigley Ave. Storm Outlet	Miller, H.M. Construction Co.	12/19/2006	1/16/2007	\$792,414.50
Stubbs Justice Center HVAC Record Drawing	Kauffman Plumbing and Heating	12/19/2006	1/8/2007	\$591,930.00
Stubbs Justice Center Fire Alarm	Didado, J.W. Electric, Inc.	12/19/2006	1/2/2007	\$338,629.00
Copley Road Parking RECORD DRAWINGS	Perrin Asphalt Co., Inc.	1/30/2007	2/12/2007	\$67,000.00
Manchester Road Phase 1 SUM - SR93 - 8.03	Kenmore Construction Co.	2/7/2007	4/2/2007	\$1,949,113.45
Morley Health Center Room 438	Hunter Chase Inc.	2/15/2007	3/26/2007	\$28,800.00
Street Tree Replacement 2007	Vizmeg Landscape, Inc.	2/20/2007	3/5/2007	\$170,763.58
Laird Street	Perrin Asphalt Co., Inc.	2/28/2007	3/19/2007	\$74,935.00
Kenmore Boulevard	Cioffi & Son Construction Co.	3/1/2007	3/26/2007	\$1,343,956.20
Kenmore Community Center Roof Record	Sanyo Construction	3/1/2007	3/19/2007	\$28,110.00
Citywide Sidewalks 2007	Cementech, Inc.	3/7/2007	4/16/2007	\$230,457.05
Hampton Knoll Roadway Improvements	Tri Mor Corporation	3/14/2007	4/9/2007	\$318,682.50
Howard Street	Cioffi & Son Construction Co.	3/20/2007	4/2/2007	\$2,446,735.10
Highland Square Redevelopment - Phase 4 Record	Aaron Landscape, Inc.	3/21/2007	4/2/2007	\$76,836.00
Thayer Street Record Drawing	Tri Mor Corporation	3/21/2007	4/9/2007	\$347,855.00
Elizabeth Park Court Relocation	Gironda, Vito Construction Company	3/22/2007	4/2/2007	\$357,574.10
Hartford Avenue-Nome Avenue	Cementech, Inc.	4/11/2007	5/14/2007	\$408,193.45
Pelton Avenue et al	Cioffi & Son Construction Co.	4/17/2007	5/7/2007	\$914,651.14
ADA Access 2007	Cementech, Inc.	4/19/2007	5/14/2007	\$1,033,758.00
Summit Lake Maintenance Building RECORD	Lockhart Concrete	5/3/2007	5/21/2007	\$59,399.00
Evans Ave & MSC Storage Buildings Record	Carmen Construction Co., Inc.	5/8/2007	6/11/2007	\$29,400.00
Stan Hywet Trail Improv. Proj. B	Dry Stone Conservancy	5/9/2007	6/4/2007	\$88,765.00
Spicertown Public Parking RECORD DRAWINGS	Cardinal Asphalt Co., Inc.	5/9/2007	5/29/2007	\$92,695.12
Avon Street Cul-de-Sac Record Drawing	Gironda, Vito Construction Company	5/23/2007	6/25/2007	\$84,863.25
Cascade Locks Bikeway - Phase IIA	Kenmore Construction Co.	5/30/2007	6/11/2007	\$2,747,254.25
South Main Street Parking RECORD DRAWINGS	Gironda, Vito Construction Company	5/31/2007	6/11/2007	\$997,940.60
MSC Fuel Site Canopy Replacement	Carmen Construction Co., Inc.	6/6/2007	6/25/2007	\$77,200.00
Forest Lodge Play Equipment	Carmen Construction Co., Inc.	6/6/2007	6/25/2007	\$45,820.00
Waters Park Shuffle Board Canopies	South Akron Awning Company	6/6/2007	6/18/2007	\$8,750.00
Imperial Electric Cleanup Record Drawings	O.B.O. Demolition & Construction, Inc.	6/7/2007	7/30/2007	\$265,000.00
MSC Building #2 Waterproofing Record	C. Crump, Inc.	6/12/2007	7/23/2007	\$86,500.00
S. Broadway Street Traffic Signal	Perram Electric	6/27/2007	7/30/2007	\$73,140.10
Tot Lot Rehabilitation 2007	Sanyo Construction	7/3/2007	7/30/2007	\$37,353.00

Monday, April 28, 2008

Project Name	Contractor	Bid Date	Award Date	Construction Amount
Lock 3 North Public Improve. PH 1 RECORD	Kenmore Construction Co.	7/10/2007	7/16/2007	\$749,487.00
Hope 6 Public Improvements Phase 2	Kenmore Construction Co.	8/15/2007	8/27/2007	\$934,132.55
Stubbs Justice Center ADA Restrooms	DSV Builders, Inc.	8/16/2007	8/27/2007	\$82,000.00
Arcadia Rd. Canton Water JEDD	Cioffi & Son Construction Co.	8/22/2007	9/4/2007	\$115,520.00
Middlebury East Recovery Wells	H.A.D. Inc.	8/29/2007	10/9/2007	\$130,278.00
Joy Park Lighting	Thompson Electric	9/11/2007	9/24/2007	\$109,081.00
Morley Auditorium Renovation	State Wide Contractors, LLC	9/12/2007	10/1/2007	\$58,552.00
Misc Storm Improvements 2007	Delta Asphalt, Inc.	9/19/2007	10/15/2007	\$279,003.00
Edgewood Hope 6 - Phase I	Akron Metropolitan Housing Authority -	10/3/2007	10/15/2007	\$2,503,278.00
White Pond Drive Phase 1	Cioffi & Son Construction Co.	10/9/2007	10/29/2007	\$2,871,576.89
Memorial Parkway Tree Removal	Barberton Tree Service, Inc.	11/1/2007	11/13/2007	\$18,801.97
Bellfield Avenue Sanitary Sewer	Campbell Contracting Co.	11/13/2007	12/17/2007	\$241,865.00
Sanitary Sewer Reconstruction 2007	Kenmore Construction Co.	11/14/2007	11/19/2007	\$407,808.25
Memorial Parkway Tree Removal - PH 2	Barberton Tree Service, Inc.	11/27/2007	12/10/2007	\$18,275.97
Incubator-Accelerator Roof	Sommers Roofing, Inc.	11/29/2007	12/17/2007	\$385,890.00
Total Amount of 2007 Awarded Contracts				\$26,065,768.27

Monday, April 28, 2008

2007 Emergency Contract Construction Cost

	Project Name	Contractor	Construction Amount	Supplement Number	Supplement Cost	Total Contract Amount
2007-001-00	Rack 29 Emergency Repair	Kenmore Construction Co.	\$286,877.61		\$0.00	\$286,877.61
2007-038-00	MIS Air Conditioning - Emergency	Air Comfort, Inc.	\$206,165.00	1	\$19,457.00	\$225,622.00
2007-046-00	CSO Rack 13 Outfall - Emergency	Kenmore Construction Co.	\$137,952.49		\$0.00	\$137,952.49
2007-061-00	Accelerator Repairs - emerg	Meccon, Inc.	\$82,178.53		\$0.00	\$82,178.53
2007-065-00	Sherwood Dr Retaining Wall Emerg	Kenmore Construction Co.	\$53,754.37		\$0.00	\$53,754.37
2007-071-00	Main Street Bus Shelters - Emerg	Kenmore Construction Co.	\$182,696.07		\$0.00	\$182,696.07
2007-079-00	O'Neil's Duct Work Repair - Emerg	Cavanaugh Building Corporati	\$26,496.72		\$0.00	\$26,496.72
2007-082-01	Howe House Annex Demolition - Emer	Carmen Construction Co., Inc.	\$78,033.90	1	\$73,379.98	\$151,413.88
2007-083-00	I-76 Ramp Culvert - Emergency	Kenmore Construction Co.	\$119,130.17		\$0.00	\$119,130.17
2007-084-00	Romig Road Median - Emerg	Gironda, Vito Construction Co	\$266,000.00		\$0.00	\$266,000.00
						\$1,532,121.84



AEB Memorandum

To: James P. Weber, P.E.
Construction Division Manager

CC: D. Celik, M. Madonio, T. Capper, Bridge File, Construction Division File

From: Michael D. Huber
Materials Lab Supervisor *MDH*

Date: October 5, 2007

Subject: 2007 Bridge Inspection Summary

The following report is a summary of the 2007 bridge inspection. There are 100 bridges for which the City has inspection and maintenance responsibility. This is an increase of five bridges added along the bike trails. The general appraisal ratings of these bridges are listed below. For comparison, the 2004-2006 ratings are also shown.

	<u>2007</u>	<u>2006</u>	<u>2005</u>	<u>2004</u>
Critical Condition	00	00	00	00
Serious Condition	02	02	02	02
Poor Condition	03	03	01	03
Fair Condition	03	02	03	03
Satisfactory Condition	30	30	30	31
Good Condition	16	16	18	16
Very Good Condition	46	42	41	30

The following bridges are in serious condition and need attention within three years.

- No. 117 Mill Street over Railroad
Design to reconstruct the existing bridge is complete. Construction is scheduled for 2009 as an ODOT/LPA project. Steps to temporarily shore up the west abutment were made in 2005.
- No. 164 Market Street over Kelly Avenue
Project sold in early 2006 with E. Market Street Widening. Construction of a new deck and superstructure is taking place in 2007.

The following bridges are in poor condition and need attention within three years. Some of these may already be in various stages of programming, design and bidding.

- No. 109 State St. over Ohio Canal
Repair undermined slope protection west end. Study of piers for structural integrity has been completed. Municipal Bridge Funds application submitted in 2006 and 2007, for the replacement of the entire structure. Neither application was successful. ODOT feels that the structure's current condition does not warrant replacement at this time.
- No. 140 Newton Street over Roosevelt Creek
Study for possible deck replacement
- No. 154 Abington Road over Springfield Lake Outlet
Replace deck, back walls and approaches. Repair abutments and paint all steel members. Line item in 2005 Budget for plan preparation to replace bridge submitted as an Issue 2 project June 2005. Construction scheduled in 2008.

The following bridges are in fair condition and need attention within five years. Some of these may already be in various stages of programming, design and bidding.

- No. 86 Swinehart Ave over Mud Run
Replace Box beams 3 to 5 years.
- No. 113 Stuber Street over Little Cuyahoga River
Repair concrete backwalls, abutments, and wingwalls. Replace approach walks and expansion joints. Paint all steel members. Consider concrete deck overlay deck.
- No. 127 Hilbish Ave over Springfield Lake Outlet
Replace concrete deck. Rehabilitate backwalls, abutments, wingwalls and paint steel superstructure.

There are 21 railroad bridges which were inspected by the City this year. This is an increase of two bridges added for railroads that span the Cascade Locks Bike Trail. The maintenance responsibility for these bridges belongs to the respective railroad companies. The ratings are as follows:

	<u>2007</u>	<u>2006</u>	<u>2005</u>	<u>2004</u>
Critical Condition	00	00	00	00
Serious Condition	01	01	01	01
Poor Condition	07	07	07	07
Fair Condition	01	00	01	00
Satisfactory Condition	07	06	05	06
Good Condition	02	03	03	03
Very Good Condition	03	02	02	02

The following bridges are in serious condition and need attention within three years.

- No. 40 Park Street over Railroad
This structure has a posted load limit. Scope is to demo the existing 4-lane bridge without replacement. Demolition was in the 2006 Capital Budget at 100% local funds.

The following bridges are in poor condition and need attention within three years.

- No. 6R Railroad over Memorial Parkway
B & N has performed an in-depth climbing inspection and noted several deficiencies. A report has been sent to the Wheeling and Lake Erie. W & LE disagrees with the findings.
- No. 07R Railroad over Silver Street
The railroad has been notified of the bridge condition.
- No. 11R Railroad over Canal Street
The railroad has been notified of the bridge condition.
- No. 13R Railroad over Forge Street (third from west)
The railroad has been notified of the bridge condition.
- No. 19R Railroad over Newton Street
The railroad has been notified of the bridge condition.
- No. 29R Railroad over Forge Street (fourth from west)
The railroad has been notified of the bridge condition.

No. 36R Railroad over Eastwood Avenue
The railroad has been notified of the bridge condition.

The following bridges are in fair condition and need attention within five years.

No. 48R Railroad over Cascade Locks Bikeway @ MI 37
The railroad has been notified.

There are 47 other bridges for which ODOT has inspection responsibility and the City has maintenance responsibility. These bridges were also inspected by the City to assess maintenance needs. The general appraisal of these bridges is as follows:

	<u>2007</u>	<u>2006</u>	<u>2005</u>	<u>2004</u>
Critical Condition	00	00	00	00
Serious Condition	00	00	00	00
Poor Condition	00	00	00	00
Fair Condition	02	02	02	04
Satisfactory Condition	21	17	17	19
Good Condition	09	12	13	13
Very Good Condition	15	16	15	10

The following bridges are in fair condition and need attention within five years. Some of these may already be in various stages of programming, design and bidding.

No. 98 Manchester Rd over RR and W. Wilbeth Rd
Repair concrete abutments, backwalls and slope protection. Repair rockers, blast and paint superstructure.

No. 179 Dart Ave. over Ohio Canal
Study void in wearing surface and impact on box beams. Consider replacement of concrete box beams with Consplan Bridge. Repair slope protection and repair gas main supports.

There were 75 other bridges inspected by the City of Akron for which ODOT has inspection and maintenance responsibility. The general appraisal of these bridges is as follows:

	<u>2007</u>	<u>2006</u>	<u>2005</u>	<u>2004</u>
Critical Condition	00	00	00	00
Serious Condition	00	01	01	00
Poor Condition	02	04	04	03
Fair Condition	07	07	07	09
Satisfactory Condition	22	24	24	23
Good Condition	15	18	18	13
Very Good Condition	29	27	27	20

The following bridge is in poor condition and needs attention within three years. Some of these may already be in various stages of programming, design and bidding.

No. 5 Pickford Ave Pedestrian Bridge over I-77
Replace deck and fence over I-77 only. Rehabilitate concrete substructure. Blast and paint steel superstructure. Project sold in early 2006. Bridge is currently under construction.

- No. 14 W. Expressway I-77 over Boulevard Street
Repair or replace expansion joint. Repair spalled concrete backwalls, abutments and settled slope protection. Repair bearings, blast and paint superstructure

The following bridges are in fair condition and need attention within five years. Some of these may already be in various stages of programming, design and bidding.

- No. 18 I-77 over High St, Broadway St. and RR
Repair rockers and blast and paint steel superstructure. Replace settled and broken concrete slope protection
- No. 18A I-76/77 Off ramp WB over High St and Voris
Blast and paint steel superstructure. Repair or replace rockers, plates and expansion joints. Repair slope protection and curbs.
- No. 18B I-77 Ramp EB over Swietzer St, Broadway St. and RR
Repair rockers and blast and paint steel superstructure. Repair or replace rockers, plates and expansion joints. Repair slope protection and curbs.
- No. 23 I-76/77 EB over Spicer and Johnston Streets
Repair concrete backwalls, abutments, slope protection and blast and paint steel superstructure. Remove or repair east bound expansion joint at east end.
- No. 24 I – 76 over Inman Street
Repair concrete backwalls, abutments, slope protection and piers. Study possible overlay or deck replacement and repair of expansion joints
- No. 25 I-77 NB Ramp over Johnston Street
Repair concrete backwalls, abutments, slope protection and piers. Study possible overlay or deck replacement and repair of expansion joints
- No. 81 Edwin Ave Pedestrian Bridge over I-277
Repair concrete approach walks, abutments and piers. Paint all steel members.

The following bridges were rated in satisfactory to good condition overall. However these bridges need attention to one or more components within three years to continue to function in good condition. Some of these may already be in various stages of programming, design and bidding. Bridges listed are a combination of City and ODOT responsibility.

- No. 3 White Pond Drive over I – 77 West Expressway
Repair undermining of approach walks and wingwalls and guardrail.
- No. 10 East Ave over West Expressway I – 77
Repair concrete curbs, abutments and piers.
- No. 12 I-77 over Manchester Rd
Make concrete repairs to abutments and backwalls. Blast and paint steel superstructure.
- No. 13 I – 77 over Bowery St.
Replace concrete deck and patch abutments, backwalls and piers.
- No. 16 I-77 over Main St,
Repair settled and broken slope protection. Blast and paint steel superstructure.

- No. 17 I-77 on ramp over Main St, from Broadway
Repair settled and broken slope protection. Blast and paint steel superstructure. Study deck replacement.
- No. 51 Cole Ave over I – 77
Repair settled and broken concrete curbs and sidewalks. Paint superstructure
- No. 53 LaFollette over I-77
Repair damaged guardrail NE, NW, and replace settled or broken curbs and sidewalks. Blast and paint superstructure.
- No. 63 SR 8 Viaduct over North St. and Cuyahoga River
Repair erosion at pier No. 7 NE. ODOT project programmed will provide a deck overlay; repair erosion, abutment, pier, drainage and guardrail repairs; and paint the bridge. Construction scheduled for 2008.
- No. 68 I-76 Kenmore Leg over RR
Repair concrete backwalls, and abutments. Repair outside fascia beam # 15. Study erosion and differential settlement of backwall and wingwall SW and monitor beams that are crowding backwalls.
- No. 69 I – 76 Kenmore Leg over Wilbeth Rd
Replace or repair west approach slab west bound that is moving vertically under truck loading. Repair settled slope protection and guardrail, repair concrete piers and backwalls.
- No. 71 I – 76 Kenmore Leg over Battles Avenue
Overlay bridge deck west bound with micro-silica concrete and repair settled slope protection.
- No. 75 Kenmore Expressway O/ Morse Rd
Repair spalled and delaminated concrete deck, abutments and slope protection.
- No. 77 27th St over I – 76
Repair concrete piers and study possible deck overlay
- No. 80 I-277/ 224 over Manchester Road
Concrete repairs on abutments, piers, and backwalls
- No. 84 27th St. over Kenmore Blvd and RR
Replace north expansion joint, repair north concrete backwall and abutment.
- No. 92 Channelwood Pedestrian O/ Ohio Canal South Bridge
Replace rotted floor beams and wood decking at east pier.
- No. 93 Channelwood Pedestrian O/ Ohio Canal North Bridge
Replace floor beams and loose floor planks near mid-span and north edge.
- No. 94 Martha Ave over Little Cuyahoga River
Study settlement of sidewalks, pavement and parapets.
- No. 85 I-277/US - 224 over Arlington Street
Overlay bridge deck eastbound with Micro-silica concrete. May be a candidate for bridge maintenance program funds or programmed for ODOT BR funds.
- No. 101 S. Main St. over CSX and Conrail RR
Structure will need to be rehabilitated with a new concrete deck, expansion joints, and approach slabs along with paint and repairs to concrete backwalls, abutments and piers in 5 to 8 years.

- No. 102 Miller Ave over CSX and Conrail RR
Structure will need to be rehabilitated with a new concrete deck, expansion joints, and approach slabs along with repairs to concrete backwalls, abutments and piers in 5 to 8 years.
- No. 104 Rhodes Ave over Ohio Canal
Replace north approach slab, repair expansion joints, and repave approach pavements.
- No. 114 Thornton St over RR
Perform temporary repairs to prevent loss of fill through deteriorated joint at interface between wingwall and abutment at NE corner. Resurface deck with micro-silica overlay, repair or replace expansion joints, replace approach slabs and make repairs to wingwalls NE and SE, patch abutments and piers, reset and maintenance rocker bearings.
- No. 116 University Avenue over RR
Repair frozen rocker bearings.
- No. 120 Palisades Drive over RR
Study MSE Wall displacement to determine structural integrity.
- No. 121 Waterloo Rd. O/ Brewster Run
Clean out channel and inside both pipe.
- No. 124 Triplett Blvd. (SR 764) over RR
Repair concrete piers and abutments. Repair settled sidewalks and replace concrete approach slabs. Replace bearings on east end that are allowing excessive vertical movement and paint all steel members.
- No. 126 Wedgewood Ave over Springfield Lake Outlet
Repair settled and broken sidewalks and curbs.
- No. 129 Brittain Rd O/ E. Market St. (SR 18)
Rehabilitate backwalls, abutments, wingwalls and parapet walls. Replace expansion joints, reset bearings and paint steel superstructure.
- No. 132 Goodyear Blvd O/RR –
Repair erosion of slope protection at all four corners.
- No. 133 East Market St. (SR 18) over RR at Case Ave
Repair or replace expansion joints, repair spalled backwalls and abutments.
- No. 136 Arlington St. over W& LE RR
Sandblast and Paint 2007 Bridge Maintenance Program funds will be used to paint this bridge. Work likely to occur in 2008.
- No. 147 Martha Ave O/ ABBR RR
Study cause of displacement and settling problems of sidewalk and parapets. This should be done in conjunction with adjacent bridge # 94 Martha Ave O/ Little Cuyahoga River.
- No. 148 Brittain Rd. over RR @ E. Market St.
Rehabilitate backwalls and abutments, replace concrete box beams, deck and expansion joints.
- No. 149A All America (Y-bridge) (SR 261) SB over North St.
Remove loose concrete from floor. Study possible deck replacement and repair expansion joints. Repair spalling at the top of the parapet walls.

- No. 149 All America (Y-bridge) (SR 261) SB over North St.
Remove loose concrete from floor. Study possible deck replacement and repair expansion joints. Repair spalling at the top of the parapet walls.
- No. 153 Thornton O/ Ohio Canal
Repair or replace cracked, broken or spalled sidewalks and curb. Repair or replace concrete deck and repair concrete abutments. An application for Municipal Bridge Funds was submitted in 2007 for rehabilitation of the bridge. The application was not successful.
- No. 160 Mill St O/ Cascade Parking Deck
Study crack in beam east of the Edison and Cascade entrance. Crack is horizontal and open more than 1".
- No. 162 Kelly Ave O/ Little Cuyahoga
Repair or replace cracked, broken or spalled sidewalks and curb. Concrete box beam deck should be studied for replacement.
- No. 165 Market Street (SR 18) over Innerbelt (SR 59)
Repair concrete Sidewalks, backwalls, abutments, blast and paint all steel members. ODOT will paint this bridge in 2008.
- No. 166 Ramp B over SR 59 Innerbelt
Replace concrete backwalls, repair abutments, repair and reposition rockers, and paint superstructure. ODOT will paint this bridge in 2008.
- No 167 Ramp A over SR 59 Innerbelt
Replace concrete backwalls, repair abutments, repair and reposition rockers, and paint superstructure. ODOT will paint this bridge in 2008.
- No. 171 SR 59 Innerbelt over Exchange St.
Replace backwalls, expansion joints and bearings. Repair abutments and paint or replace superstructure. Replace approach slabs and study deck replacement.
- No. 174 Innerbelt SR 59 over Cedar St
Repair settled slope protection.
- No. 177 Wooster Ave O/ SR 59 Innerbelt
Repair approach sidewalk NE, NW, and SW.
- No. 178 Bartges over SR 59 Innerbelt
Repair settled and broken sidewalks and curbs; clean and repair rockers.
- No. 183 SR 59 O/ Dart, Thornton, and Ohio Canal
Repair and paint rockers. Repair settled and broken slope protection.
- No. 184 SR 59 O/ Dart, Thornton, and Ohio Canal
Repair settled and broken slope protection.
- No. 185 SR 59 Innerbelt Ramp over I – 76 NB
Repair west expansion joint. Clean and realign rockers.

MDH/mm

Number of Mapping/GIS Requests Made To Cartographer & Who Requested For 2007

- Total number of requests is 234
 - Engineering = 53 plus created bridge geodatabase
 - Economic Development = 104
 - Mayor's Office = 43 plus created mowing geodatabase (includes Marathon & Goodyear requests)
 - Public Works = 22 plus created mowing geodatabase
 - Prosecutor's Office = 6
 - Planning = 3
 - Fire Department = 2
 - Police Department = 1

Akron Engineering Bureau

Project Reports 2007



<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Abington Rd. o/ Spring. Lake Outlet	2004-007-00	

<i>Description</i>
Project Objective: To replace or rehabilitate the bridge structure. Project Limits: Abington Road at Springfield Lake Outlet.

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase II	2/26/2007	7/30/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Abington Road Fencing	2006-062-00	

<i>Description</i>
Project Objective: Install security fence on City-owned property on Abington Road. Work will be done in conjunction with fencing done by the Abington Road Condominiums. Project Limits: From Abington Road west, approximately 700 feet across the City property, then north approximately 350 feet along the west property line of the condominium development.

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Construction Phase	11/13/2007	11/27/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Accelerator Repairs - emerg	2007-061-00	

<i>Description</i>
Project Objective: Replace overtaxed condensate pumps to eliminate a flooding problem, replace failed fire suppression water line, repair roof drain to eliminate a flooding problem, and replace an existing air handler to restore air conditioning to the first floor. The contractor is Mecon, Inc. Project Limits: Accelerator, 526 South Main Street

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Construction Phase	6/11/2007	7/13/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
ADA Access 2007	2007-041-00	

<i>Description</i>
Project Objective: Install ADA compliant curb ramps as required by law and related with the resurfacing program. Project Limits: City wide

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	3/13/2007	3/13/2007
Construction Phase	7/9/2007	12/14/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
ADA Access 2007	2007-041-00	

Description

Project Objective: Install ADA compliant curb ramps as required by law and related with the resurfacing program.
Project Limits: City wide

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	3/13/2007	3/13/2007
Construction Phase	7/9/2007	12/14/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Arcadia Rd. Canton Water JEDD	2006-019-00	

Description

Project Objective: Design and construction of a water line on Arcadia Road from Canton Road to Waterloo Road.
Project Limits: Arcadia Road from Canton Road to Waterloo Road.

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Construction Phase	10/15/2007	11/23/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Avon Street Cul-de-Sac Record Drawing	2007-007-00	

Description

Project Objective: To eliminate the Avon/Howard intersection
Project Limits: Avon Street from Howard Street to Creston Avenue

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	2/1/2007	3/2/2007
Construction Phase	9/17/2007	10/19/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Avon Street Cul-de-Sac Record Drawing	2007-007-00	

Description

Project Objective: To eliminate the Avon/Howard intersection
Project Limits: Avon Street from Howard Street to Creston Avenue

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	2/1/2007	3/2/2007
Construction Phase	9/17/2007	10/19/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Balch Auditorium Improvements Record Drawing	2004-064-00	

Description

Project Objective: Renovate portions of the back stage and dressing / storage rooms and the auditorium.
Project Limits: The Balch Street Community Center Auditorium and back stage spaces.

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Construction Phase	5/10/2007	7/20/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Bartges Street/Towpath Underpass	2005-016-00	

Description

Reconstruction of the Bartges Street Bridge over the Ohio & Erie Canal including relocation of existing utilities off of the bridge. The new structures include a 36' wide span over the canal and an adjacent 16' wide span for the Ohio & Canal Towpath Trail. Both spans will be a pre-manufactured modular concrete structures. Issue 2 application in 2005. Oups Reference # 0203036048

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	1/22/2007	6/9/2009

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Bridge Painting 2007	2007-063-00	

Description

Project Objective: Painting of steel beams on the N. Arlington Bridge over the W&LE Railroad.
Project Limits: Steel superstructure of Bridge #136, N. Arlington over W&LE RR.

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	6/22/2007	8/7/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Buchtel - College Signalization	2007-087-00	

Description

Project Objective: To add traffic signal and pedestrian signals to the intersection as agreed upon by the City of Akron and University of Akron.
Project Limits: Intersection of Buchtel Avenue and College Street.

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	12/10/2007	

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Carroll Street	2005-082-00	

Description

Project Objective: To improve Carroll Street by reconstructing the pavement, curbs, sidewalk, aprons, replacing the water main and installing street trees.

Project Limits: Fountain Street to Annadale Avenue

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	12/10/2007	

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Cascade Deck Repairs Annex	2007-070-00	

Description

Project Objective: To repair and replace deteriorated concrete within the parking deck structure and recoat the decks with a waterproofing membrane in the Annex section of the garage.

Project Limits: Cascade Parking Garage

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	9/3/2007	11/7/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Cascade Deck Van Area Emergency	2008-010-00	

Description

Project Objective: To repair the failing concrete floor. The floor is now has temporary shoring to support it. Donley's Inc., was hired to make the repairs.

Project Limits: Cascade Parking Garage, in the van parking area.

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Construction Phase	11/15/2007	5/16/2008

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Cascade Locks Bikeway - Phase IIA	2004-079-00	

Description

Project Objective: Extend the Cascade Locks Bikeway across the Innerbelt to Quaker-Ash Street intersection.

Project Limits: The Towpath Trail will be extended from Beech Street in the Cascade Valley Park southerly following the west side of the Innerbelt, cross over the Innerbelt and to the intersection of Ash and Quaker streets.

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Construction Phase	7/16/2007	9/12/2008

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Central Services Facility HVAC	2006-028-00	

<i>Description</i>
Project Objective: To up-grade the existing heating, ventilating, and air-conditioning system to a more reliable system. Project Limits: Central Services Facility building Revised fund and org from 60001-MEP003 on 6/26/06

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Construction Phase	4/16/2007	6/22/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
CitiCenter Elevator Upgrade	2007-048-00	

<i>Description</i>
Project Objective: Upgrade two passenger elevators at the CitiCenter to provide improved service and to meet current ADA requirements. Project Limits: The CitiCenter building

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	11/5/2007	11/23/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
CitiCenter Parking Deck Repairs RECORD DRAWINGS	2004-017-00	

<i>Description</i>
Project Objective: Replace existing expansion joints on parking deck. Project Limits: CitiCenter Parking Deck

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Construction Phase	4/2/2007	10/19/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Citywide Sidewalks 2007	2007-009-00	

<i>Description</i>
Project Objective: To repair defective sidewalks and driveway aprons as petitioned by individual property owners. Project Limits: Various locations throughout the city.

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	1/18/2007	1/24/2007
Construction Phase	5/21/2007	7/20/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Citywide Sidewalks 2007	2007-009-00	

Description

Project Objective: To repair defective sidewalks and driveway aprons as petitioned by individual property owners.
Project Limits: Various locations throughout the city.

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	1/18/2007	1/24/2007
Construction Phase	5/21/2007	7/20/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Communications Relocation	2007-049-00	

Description

Project Objective: Renovate the building at 250 Opportunity Parkway for the Communications Division.
Project Limits: The building and site at 250 Opportunity Parkway
Project was cancelled on 6/14/07.

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	6/11/2007	7/23/2007
Construction Phase	11/7/2007	12/21/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Communications Relocation	2007-049-00	

Description

Project Objective: Renovate the building at 250 Opportunity Parkway for the Communications Division.
Project Limits: The building and site at 250 Opportunity Parkway
Project was cancelled on 6/14/07.

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	6/11/2007	7/23/2007
Construction Phase	11/7/2007	12/21/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Copley Rd. Resurfacing	2002-092-00	

Description

Copley Rd. Resurfacing - Sum-SR 162-6.11 PID 25552
Project Objective: Minor rehabilitation and resurfacing
Project Limits: I-77 to Hawkins Avenue

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Construction Phase	7/2/2007	7/31/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Copley Road Parking RECORD DRAWINGS	2005-091-00	

Description

Project Objective: To provide off street parking for local businesses.

Project Limits: On the north side of Copley Road from Hawkins Ave. to Nome Ave.

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Construction Phase	5/7/2007	6/5/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
CSO Rack 13 Outfall - Emergency	2007-046-00	

Description

Project Objective: Reconstruct the outfall pipe which has begun falling into the stream. Kenmore Construction was hired by the Service Director to make these emergency repairs.

Project Limits: The outfall is located on the Little Cuyahoga River, approximately 650 feet southeast of the intersection of E. North Street and N. Arlington Street.

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Construction Phase	4/9/2007	5/18/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Dart Ave Parking Deck Site Work	2007-003-01	

Description

Project Objective: To construct a retaining wall along Main St. and excavate site in preparation for new parking deck

Project Limits: East of Dart Ave., west of S. Main St., north of Superblock Parking Deck

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	4/12/2007	5/18/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Davenport Park Pavilion	2007-047-00	

Description

Project Objective: Proposed improvements include the renovation of the existing restroom building, sidewalk reconstruction and the construction of a pavilion.

Project Limits: Davenport Park

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	5/14/2007	1/17/2008

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Downtown Directional Signage	2007-072-00	

Description

Project Objective: Provide informational and directional signage for vehicular and pedestrians.

Project Limits: Downtown area

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	9/10/2007	1/24/2008

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Dresden Avenue	2007-032-00	

Description

Project Objective: Full Improvements

Project Limits: South Firestone Boulevard to Brown Street

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	3/15/2007	10/26/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
E. Market St. Fiber & Signalization	2007-067-00	

Description

Project Objective: To upgrade the existing intersections with poles, mast arms, LED signals, pedestrian signals, video cameras, emergency pre-emption, and fiber optic cable.

Project Limits: Goodkirk to Firestation No. 2

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	9/5/2007	4/10/2009

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
E. Market St. over Kelly Ave. & SUM-18-12.31 Part 2	2003-082-00	

Description

Project Objective: To replace the existing box beam deck that is in poor condition.

Project Limits: Bridge No. 164

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Construction Phase	4/2/2007	10/12/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
E. Market Street Sidewalks and Curb	2007-005-00	

Description

Project Objective: Reconstruct sidewalk and curb as necessary, construct bulb-outs at four corners of each intersection to establish on-street metered parking and reduce the pedestrian crossing width to improve pedestrian flow, revise lane striping and signage, plant street trees, and relocate overhead street lighting wires underground.

Project Limits: E. Market Street from Main Street to Summit Street

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	12/10/2007	1/14/2008

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Ed Davis Tennis Courts	2007-056-00	

Description

Project Objective: Reconstruction of six existing tennis courts on City of Akron property.

Project Limits: The tennis courts are located on the west side of Edgewood Avenue at the intersection of Chestnut Street.

Project is cancelled as of 7/24/2008.

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	7/27/2007	3/28/2008

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Edgewood Hope 6 - Phase I	2006-074-00	

Description

Project Objective: AMHA site redevelopment including full street improvements along several existing roadways for townhouse development. (First of three phases)

Project Limits: Phase I includes: Euclid (S. side - Raymond to Rhodes), Rhodes (Euclid to Vernon Odom), Edgewood (Euclid to Vernon Odom) & a new public street.

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Construction Phase	11/28/2007	10/31/2008

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Edgewood Hope 6 - Phase II	2006-074-01	

Description

Project Objective: AMHA site redevelopment including full street improvements along several existing roadways for townhouse development. (Second of three phases)

Project Limits: Phase II includes: Westerly Court extension (Raymond St. to Edgewood Blvd.), N-S Street (Warner Ct. to Westerly Ct.) & E-W Street (N-S St. to Edgewood Blvd).

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	12/3/2007	11/5/2008

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Elizabeth Park Court Relocation RECORD DRAWINGS	2005-049-00	

Description

Project Objective: Relocation of 3 basketball courts, 1 tennis court, 1 baseball field, play equipment and parking lot as part of Hope VI project.

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Construction Phase	5/21/2007	10/12/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Elm Drive Wigley Ave. Storm Outlet RECORD DRAWINGS	2004-020-00	

Description

Project Objective: Study and modify existing outlet to prevent flooding of E. Market Street.
Project Limits: E. Market St. to Little Cuyahoga River.

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Construction Phase	3/12/2007	10/19/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Evans Ave & MSC Storage Buildings Record Drawings	2007-016-00	

Description

Project Objective: Repair the roofs of these buildings.
Project Limits: The Evans Avenue calcium storage building and the Municipal Service Center complex infield mix storage building.

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	1/31/2007	2/13/2007
Construction Phase	7/16/2007	9/21/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Evans Ave & MSC Storage Buildings Record Drawings	2007-016-00	

Description

Project Objective: Repair the roofs of these buildings.
Project Limits: The Evans Avenue calcium storage building and the Municipal Service Center complex infield mix storage building.

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	1/31/2007	2/13/2007
Construction Phase	7/16/2007	9/21/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Fire Station #14 HVAC	2007-030-00	

Description

Project Objective: Modernize the HVAC system at Fire Station #14.
Project Limits: Fire Station #14, 766 Brittain Road

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	5/21/2007	10/19/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Fire Stations #2 & #12 Floor Repair	2007-028-00	

Description

Project Objective: Repair structurally deficient apparatus floors in these two firehouses.

Project Limits: Fire Station #2, 952 E. Exchange Street, and Fire Station #12, 1852 W. Market Street

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Construction Phase	3/1/2007	4/1/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Firestone Stadium Improvements	2004-005-00	

Description

Project Objective: To provide fencing, parking lot security lighting, paving of a drivable strip in the parking lot, and changes to the stadium seating.

Project Limits: Firestone Stadium and site.

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Construction Phase	1/8/2007	7/6/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
First Energy Detention Pond	2007-086-00	

Description

Project Objective: Design and construct a grading project so that adjacent surface water can be directed towards an existing basin

Project Limits: Existing basin between Goldleaf Drive and Olentangy Drive

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	12/10/2007	11/10/2008

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Forest Lodge Play Equipment	2007-026-00	

Description

Project Objective: Replace existing intermediate play equipment, soft surface, and drainage with new up-to-date equipment and materials.

Project Limits: Forest Lodge Park.

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	2/26/2007	4/20/2007
Construction Phase	9/4/2007	10/12/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Forest Lodge Play Equipment	2007-026-00	

Description

Project Objective: Replace existing intermediate play equipment, soft surface, and drainage with new up-to-date equipment and materials.

Project Limits: Forest Lodge Park.

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	2/26/2007	4/20/2007
Construction Phase	9/4/2007	10/12/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Hampton Knoll Roadway Improvements	2006-050-00	

Description

Project Objective: To reconstruct Hampton Knoll Drive with asphalt pavement, concrete curb and gutter and updated storm sewers.

Project Limits: From Akron-Peninsula Road to 950 feet northeast to cul-de-sac.

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Construction Phase	5/14/2007	6/27/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Hartford Avenue-Nome Avenue RECORD DRAWINGS	2004-095-00	

Description

Project Objective: To construct full street improvements.

Project Limits: Hartford Avenue from Tacker Road to Courtland Avenue; Nome Avenue from Lawton Street to Copley Road.

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Construction Phase	7/9/2007	11/2/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Hickory Street Phase 2 - Roadway Improvements	2004-044-00	

Description

Project Objective: Full street improvements by grading, paving, curb and sidewalk and street trees.

Project Limits: Hickory Street (Walnut St. to Howard St.)

Walnut St. (Hickory St. to W. North St.)

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	12/3/2007	

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Hickory Street Phase 2 - Utility Improvements	2004-044-01	

Description

Project Objective: Construction of storm and sanitary sewers, water main relocation, underground utilities and street lighting.
Project Limits: Hickory Street (Walnut St. to Howard St.)
Walnut St. (Hickory St. to W. North St.)
The fund and org was 42245-VF0706 revised on 1/31/08 to the assessable fund and org. This project was cancelled on 2/19/08, and will be performed under AEB# 2004-044-00

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	5/30/2007	1/21/2008

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Highland Square Redevelopment - Phase 4 Record Drawings	2005-095-03	

Description

Project Objective: To install landscaping features within the Highland Square Redevelopment Area.
Project Limits: (see attached map)

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Construction Phase	5/21/2007	6/8/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Hope 6 Public Improvements Phase 2	2005-050-00	

Description

Project Objective: Plans for Phase 2 of public improvements in support of Hope VI housing project. Construction scheduled for 2007.
Project Limits: South of North Street, between Spring St (W) and Spring St (E). Spring St. from North St. to Spring Court and Sprint Court back to North St., Stuber St. from Spring Ct. to North St., Cascade Ct. from Spring Ct. to North St., North St. from Sta. 12+00 to 17+50 to Spring Ct.

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Construction Phase	11/5/2007	6/27/2008

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Howard Street	2004-008-00	

Description

Project Objective: Full Improvements
Project Limits: Lods Street to Cuyahoga Falls Avenue

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Construction Phase	6/4/2007	8/15/2008

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Howard Street Sanitary Repair Emergency	2008-019-00	

Description

Project Objective: Emergency repairs on collapsed 10 inch and 12 inch sanitary sewers.
Project Limits: N. Howard Street at the intersection of Cuyahoga Street.

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Construction Phase	9/11/2007	12/21/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Hyre Park Tennis Court Resurfacing	2007-081-00	

Description

Project Objective: Resurface the tennis courts at Hyre Park.
Project Limits: Eight existing tennis courts at Hyre Park.

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	11/5/2007	2/15/2008

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
I-76 Ramp Culvert - Emergency	2007-083-00	

Description

Project Objective: Replace failing culvert. Contractor is Kenmore Construction.
Project Limits: I-76 eastbound ramp to Kenmore Leg

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Construction Phase	10/26/2007	11/10/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
I-77 & I-277 Resurfacing	2002-093-00	

Description

Project Objective: Minor rehabilitation and resurfacing on I-77 and I-277
Project Limits: I-77 (Central Interchange to Swartz Rd.) I-277 (Waterloo Rd. to I-277)

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Construction Phase	7/2/2007	7/31/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Imperial Electric Cleanup Record Drawings	2007-043-00	

Description

Project Objective: Conduct demolition, cleanup, and disposal of hazardous material at the former Imperial Electric property which was damaged by fire in 2004.

Project Limits: Former Imperial Electric property, 84 Ira Avenue.

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	3/19/2007	3/23/2007
Construction Phase	8/20/2007	9/28/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Imperial Electric Cleanup Record Drawings	2007-043-00	

Description

Project Objective: Conduct demolition, cleanup, and disposal of hazardous material at the former Imperial Electric property which was damaged by fire in 2004.

Project Limits: Former Imperial Electric property, 84 Ira Avenue.

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	3/19/2007	3/23/2007
Construction Phase	8/20/2007	9/28/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Incubator-Accelerator Roof	2007-010-00	

Description

Project Objective: Replace the low slope roofing system.

Project Limits: The Incubator/Accelerator, 526 South Main Street, Building 5

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	4/16/2007	6/8/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Joy Park Lighting	2007-051-00	

Description

Project Objective: Replace existing lighting at the basketball and tennis courts.

Project Limits: Joy Park

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	6/4/2007	7/16/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Kenilworth Drive	2005-073-00	

Description

Project Objective: To reconstruct existing street.

Project Limits: Kenilworth Drive from Greenvale Avenue to Garman Road.

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	6/25/2007	6/25/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Kenmore Boulevard	2005-015-00	

Description

Project Objective: The objective of the project is to improve Kenmore Boulevard by grinding and resurfacing asphalt pavement, reconstructing sidewalk, curb, drive aprons, house drains, and retaining walls, replacing all sidewalk street trees, replacing center median street trees as necessary, removing portions of center medians extending into the paths of marked cross walks, reconstructing center median perimeter curb as necessary, installing pedestrian-level street lighting and 2 foot brick lawn strip adjacent to the curb within the Kenmore Business District, extending a 16" feeder main from 19th Street to 20th Street, and installing a traffic signal at the 19th Street/I-76 Ramp intersection.

Project Limits: 11th Street to 20th Street

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Construction Phase	4/23/2007	12/18/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Kenmore Community Center Roof Record Drawings	2006-043-00	

Description

Project Objective: The project involves the repair of a roof leak and also to repair or replace interior cabinet doors.

Project Limits: The project limit is the roof and the building interior.

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Construction Phase	6/7/2007	7/21/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Killian Rd. Conlin Water JEDD	2006-014-00	

Description

Project Objective: Design and construction of a water line on Killian Road from S. Main Street to Conlin Drive.

Project Limits: Killian Road from Conlin Drive to S. Main Street.

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Construction Phase	1/11/2007	5/11/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Kirn Street (Crouse St. to Power St.)	2005-024-00	

Description

Spicer town Public Improvements

Project Objective: Public Improvements in Spicer town to support University Park Alliance. This request includes Pedestrian Walkways also shown in the budget under a separate line item for \$200,000.

Project Limits: Kirn Street (Crouse St. to Power St.) & Pedestrian Walkways adjacent to new Kirn.

This project was performed under the Brown St., Power St., and Kirn St., Improvements project, AEB #2005-022-00

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	10/8/2007	10/25/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Laird Street	2004-096-00	

Description

Project Objective: To construct concrete combined curb and gutter, concrete drive approaches, concrete sidewalks, full depth asphalt pavement, water services where required and tree planting and removal where required.

Project Limits: Laird Street from Martha Avenue to Barder Avenue

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Construction Phase	6/4/2007	8/10/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Lake of the Woods Pump Station	2007-015-00	

Description

Project Objective: Replace the existing pump station.

Project Limits: 600 Lake of the Woods Drive.

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	2/6/2007	10/26/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Landmark Garage Demo	2006-047-00	

Description

Project Objective: To remove the Landmark parking structure.

Project Limits: Landmark Parking Garage located adjacent to Bowery Street west of Main Street.

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Construction Phase	2/20/2007	4/6/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Legacy Development	2007-076-00	

Description

Project Description: Construction of a traffic signal at the intersection of Market Street and Prospect Street.

Project Limits: E. Market St. Prospect Street Intersection

Designed by GPD, **Bid and Constructed by** Developer, **Inspected by** Engineering Bureau

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Construction Phase	11/12/2007	12/28/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Lisa Ann Park Rehabilitation	2007-060-00	

Description

Project Objective: Park rehabilitation. Include new play equipment, swings, soft surfacing, dirt bike mounds.

Project Limits: Ivor Ave. (Janis Ave. to Clearfield Ave.)

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	6/6/2007	9/20/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Lock 3 ADA Access - Emergency	2008-029-00	

Description

Project Objective: Work required to construct an ADA access security door in the basement level of the O'Neil's building. This project was deemed an emergency due to requirements of completion by November 26, 2007, or before the City of Akron Holiday Fest began.

Project Limits: Basement level of the O'Neil's building.

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Construction Phase	11/1/2007	11/26/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Lock 3 North Public Improve. PH 1 RECORD DRAWINGS	2004-058-02	

Description

Project Objective: The project consists of Phase 1 of the redevelopment of the area downstream of the Ohio and Erie Canal's Lock 3, southwest of the corner of Bowery Street and Main Street. This includes removal of the canal enclosure for approximately 100 feet, tying back the canal walls, the construction of small retaining walls and headwall to support the grading adjacent to the canal enclosure removal, the relocation of the canal's odor control buildings and a sanitary sewer relocation.

Project Limits: The Lock 3 North Public Improvements located along the Ohio and Erie Canal bound by Bowery St/Cascade Deck to the north and Lock 3 and Civic to the south.

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	3/19/2007	5/2/2007
Construction Phase	8/20/2007	12/21/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Lock 3 North Public Improve. PH 1 RECORD DRAWINGS	2004-058-02	

Description

Project Objective: The project consists of Phase 1 of the redevelopment of the area downstream of the Ohio and Erie Canal's Lock 3, southwest of the corner of Bowery Street and Main Street. This includes removal of the canal enclosure for approximately 100 feet, tying back the canal walls, the construction of small retaining walls and headwall to support the grading adjacent to the canal enclosure removal, the relocation of the canal's odor control buildings and a sanitary sewer relocation.

Project Limits: The Lock 3 North Public Improvements located along the Ohio and Erie Canal bound by Bowery St/Cascade Deck to the north and Lock 3 and Civic to the south.

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	3/19/2007	5/2/2007
Construction Phase	8/20/2007	12/21/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Lock 3 North Public Improve. PH 2	2004-058-03	

Description

Project Objective: To design and construct open space improvements to the public area along Garden Alley behind the 156-146 S. Main Street to support development.

Project Limits: The Lock 3 North Public Improvements located along the Ohio and Erie Canal bound by Bowery St/Cascade Deck to the north and Lock 3 and Civic to the south.

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	7/23/2007	9/26/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Main Street Building Renovation	2004-058-00	

Description

This project will involve the environmental/asbestos investigation and demolition of 164 - 186 South Main Street. The name of this project was revised from 'Lock 3 Redevelopment' on 10/27/2006.

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Construction Phase	1/8/2007	4/13/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Main Street Bus Shelters - Emerg	2007-071-00	

Description

Project Objective: Remove old bus shelters and planters and install new bus shelters. The new shelters are being provided by Metro. The contractor is Kenmore Construction Co.

Project Limits: Market Street to University Avenue

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Construction Phase	8/13/2007	1/11/2008

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Manchester Road Phase 1 SUM - SR93 - 8.03	2003-042-00	

Description

Project Objective: Reconstruction of pavement, curb, sidewalk, and drive aprons. Traffic signalization upgrades and drainage improvements.

Project Limits: Carnegie Avenue to Waterloo Road

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Construction Phase	4/16/2007	6/24/2008

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Market St. W., Utility Relocation Hawkins to Twin Oaks	2004-089-01	

Description

Project Objective: To relocate the overhead utilities underground from Hawkins to Twin Oaks and to reconnect all properties

Project Limits: West Market Street from Hawkins to Twin Oaks

Update: Underground utility relocations will not be performed due to cost.

Plan Status: Have 90 percent complete plans. RW needs included in 2004-089-00.

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	1/15/2007	8/28/2009

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Massillon o/Springfield Lake Outlet	1999-111-00	M-31

Description

Project Objective: Reconstruction of 0.030 miles (160 feet) of SR241 including replacement of the bridge over Springfield Lake Outlet.

ODOT constructed in 2007. PID 19924

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Construction Phase	3/5/2007	8/17/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Memorial Parkway Tree Removal	2007-033-00	

Description

Project Objective: Multi-year program to remove trees along Memorial Parkway that are affected by erosion.

Project Limits: Memorial Parkway - Evers to Aqueduct; Uhler - Cuyahoga to Memorial Parkway

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	2/28/2007	3/1/2007
Construction Phase	12/20/2007	1/14/2008

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Memorial Parkway Tree Removal	2007-033-00	

Description

Project Objective: Multi-year program to remove trees along Memorial Parkway that are affected by erosion.
Project Limits: Memorial Parkway - Evers to Aqueduct; Uhler - Cuyahoga to Memorial Parkway

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	2/28/2007	3/1/2007
Construction Phase	12/20/2007	1/14/2008

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Memorial Parkway Tree Removal - PH 2	2007-033-01	

Description

Project Objective: Multi-year program to remove trees along Memorial Parkway that are affected by erosion.
Project Limits: Memorial Parkway - Evers to Aqueduct; Uhler - Cuyahoga to Memorial Parkway

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Construction Phase	12/20/2007	2/29/2008

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Middlebury East Recovery Wells	2007-055-01	

Description

Project Objective: Install the recovery wells necessary to clean up the environmental contamination identified in the groundwater within the project limits.
Project Limits: City-owned properties, and the Robinson Street and railroad right-of-ways located at the northwest corner of the intersection of Arlington Street and E. Exchange Street.

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	5/14/2007	7/16/2007
Construction Phase	11/19/2007	2/29/2008

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Middlebury East Recovery Wells	2007-055-01	

Description

Project Objective: Install the recovery wells necessary to clean up the environmental contamination identified in the groundwater within the project limits.
Project Limits: City-owned properties, and the Robinson Street and railroad right-of-ways located at the northwest corner of the intersection of Arlington Street and E. Exchange Street.

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	5/14/2007	7/16/2007
Construction Phase	11/19/2007	2/29/2008

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Middlebury East Remedial System	2007-055-02	

Description

Project Objective: To install, operate, and maintain the remedial pumping system that is needed to clean up the groundwater contamination identified within the project limits.

Project Limits: City-owned properties, and the Robinson Street and railroad right-of-ways located at the northwest corner of the intersection of Arlington Street and E. Exchange Street.

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	5/14/2007	8/10/2007
Construction Phase	11/19/2007	12/29/2008

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Middlebury East Remedial System	2007-055-02	

Description

Project Objective: To install, operate, and maintain the remedial pumping system that is needed to clean up the groundwater contamination identified within the project limits.

Project Limits: City-owned properties, and the Robinson Street and railroad right-of-ways located at the northwest corner of the intersection of Arlington Street and E. Exchange Street.

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	5/14/2007	8/10/2007
Construction Phase	11/19/2007	12/29/2008

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Mill Street Sewer Relocation	2004-088-00	

Description

Project Objective: Relocation of combined sewer; full improvements on College Street; related to Mill Street bridge replacement.

Project Limits: Mill Street: Lincoln to College

College Street: Mill to Market

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	6/18/2007	5/1/2008

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
MIS Air Conditioning - Emergency	2007-038-00	

Description

Project Objective: Replace four air conditioning units that are no longer capable of keeping the computers within their required operating temperature. The contractor is Air Comfort, Inc.

Project Limits: Municipal Building 8th floor

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Construction Phase	6/1/2007	8/31/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Misc Storm Improvements 2007	2007-017-00	

Description

Project Objective: Miscellaneous improvements to areas which experience flooding due to storm water drainage problems.
Project Limits: Stoner Avenue (Storer-Mercer) - Flooding caused by dead inlets. Brice Road (2551) - Storm water missing existing inlets and causing flooding. Winhurst - Storm pipe lined - no longer meets capacity. Chester (Smith Elementary) - Dangerous sidewalk due to constant wet conditions. Clearview Avenue - housedrain icing street. Foxboro Avenue - replace undersized culvert. Malasia Park -flooding makes the park unusable. Preston Avenue - water runoff in street. Miscellaneous spots on Brewster creek -erosion problems.

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	4/2/2007	7/20/2007
Construction Phase	11/26/2007	6/13/2008

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Misc Storm Improvements 2007	2007-017-00	

Description

Project Objective: Miscellaneous improvements to areas which experience flooding due to storm water drainage problems.
Project Limits: Stoner Avenue (Storer-Mercer) - Flooding caused by dead inlets. Brice Road (2551) - Storm water missing existing inlets and causing flooding. Winhurst - Storm pipe lined - no longer meets capacity. Chester (Smith Elementary) - Dangerous sidewalk due to constant wet conditions. Clearview Avenue - housedrain icing street. Foxboro Avenue - replace undersized culvert. Malasia Park -flooding makes the park unusable. Preston Avenue - water runoff in street. Miscellaneous spots on Brewster creek -erosion problems.

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	4/2/2007	7/20/2007
Construction Phase	11/26/2007	6/13/2008

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Morley Auditorium Renovation	2007-050-00	

Description

Project Objective: Renovate the auditorium by doing the following: Clean/replace ceiling, repair walls and paint; replace floor tiles; replace light fixtures; replace cabinets and countertop in kitchenette area.
Project Limits: This project is limited to the Morley Health Center auditorium area which includes the kitchenette, storage room, and stage.

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	5/28/2007	6/8/2007
Construction Phase	11/13/2007	1/25/2008

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Morley Auditorium Renovation	2007-050-00	

Description

Project Objective: Renovate the auditorium by doing the following: Clean/replace ceiling, repair walls and paint; replace floor tiles; replace light fixtures; replace cabinets and countertop in kitchenette area.

Project Limits: This project is limited to the Morley Health Center auditorium area which includes the kitchenette, storage room, and stage.

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	5/28/2007	6/8/2007
Construction Phase	11/13/2007	1/25/2008

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Morley Health Center Room 438	2006-070-00	

Description

Project Objective: To renovate room 438 in the Morley Health Center, upgrading the work spaces occupied by Code Enforcement sanitarians.

Project Limits: Room 438 in the Morley Health Center

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Construction Phase	5/23/2007	6/8/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Morley North Mall Stairs	2007-029-00	

Description

Project Objective: Reconstruct crumbling steps.

Project Limits: North Mall Stairs

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	3/7/2007	4/3/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Morley Restrooms RECORD DRAWINGS	2005-021-00	

Description

Project Objective: Renovate the Morley Health Center public restrooms on each floor.

Project Limits: The Morley Health Center Building

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Construction Phase	2/8/2007	3/30/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
MSC Brine Blending Building	2007-066-00	

Description

Project Objective: Provide a wood pole type building to house new brine blending equipment.
Project Limits: The MSC complex at Triplett Boulevard

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	12/31/2007	

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
MSC Building #2 Waterproofing Record Drawings	2007-036-00	

Description

Project Objective: Waterproof the below grade walls at the north side of building #2.
Project Limits: Building #2 and its immediate site.

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	3/12/2007	4/20/2007
Construction Phase	10/1/2007	11/30/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
MSC Building #2 Waterproofing Record Drawings	2007-036-00	

Description

Project Objective: Waterproof the below grade walls at the north side of building #2.
Project Limits: Building #2 and its immediate site.

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	3/12/2007	4/20/2007
Construction Phase	10/1/2007	11/30/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
MSC Fuel Site Canopy Replacement	2006-027-00	

Description

Project Objective: Replace the old rusty canopy
Project Limits: MSC Fuel Site

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	4/9/2007	4/13/2007
Construction Phase	8/31/2007	12/24/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
MSC Fuel Site Canopy Replacement	2006-027-00	

Description

Project Objective: Replace the old rusty canopy
Project Limits: MSC Fuel Site

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	4/9/2007	4/13/2007
Construction Phase	8/31/2007	12/24/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
MSC Offices and Locker Room	2007-068-00	

Description

Project Objective: The objective for the Sanitation office is to create more office space. For the Traffic Engineering building the objective is to remodel the office area and to improve the Men's locker room.
Project Limits: MSC Sanitation office area and the Traffic Engineering Public Work area and the Men's locker room.

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	8/13/2007	10/26/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Municipal Building Floors 8 & 9	2007-014-00	

Description

Project Objective: Renovate the Municipal Building eighth and ninth floors. Floor eight is the the IT computer room and floor nine is the the IT offices. Both floors are in disrepair and require renovation.
Project Limits: The Municipal Building eighth and ninth floors.

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	10/1/2007	11/9/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
North Street Public Improvements	2005-071-00	

Description

Project Objective: To provide full street improvements to North St. from Howard St. to Furnace St. This project is Phase 3 of the Hope 6 Public Improvements.
Project Limits: North Street (Howard St. to Furnace St.)

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	12/3/2007	5/9/2008

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
ODNR Lock 1 Maintenance Relocation	2001-062-00	O-39

Description

Relocation of ODNR facilities at Summit Lake and Lock 1 to Wilbeth Rd west of the Ohio Canal. Environmental studies and property acquisition of 5-acre parcel north of Wilbeth Rd. and west of Ohio Canal for relocation of ODNR offices and storage from Lock 1 facility and facilities at the north end of Summit Lake.

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	12/31/2007	

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
O'Neil's Duct Work Repair - Emerg	2007-079-00	

Description

Project Objective: Re-attach duct work that fell from the ceiling in the parking deck. Cavanaugh Building Corporation is the contractor.

Project Limits: O'Neil's Parking Deck

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Construction Phase	7/26/2007	8/10/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Pelton Avenue et al RECORD DRAWINGS	2003-086-00	

Description

Project Objective: Full Improvements

Project Limits: Pelton Ave. from Celtic Street to Allenford St., Westmoreland St. from Manchester Rd. to Nesmith Lake Blvd., Celtic St. from Manchester Rd. to Edwin Ave.

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Construction Phase	7/23/2007	

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Police-Sheriff Firing Range	2006-006-00	

Description

Project Objective: Provide additional indoor firing lanes at the Sheriff's training facility for Akron Police.

Project Limits: The County Sheriff's training facility.

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	5/28/2007	7/30/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Prosecutor's Office Furniture	2007-077-00	

Description

Project Objective: Reconfigure the office furniture in the Prosecutor's space to eliminate un-used cubicles, provide a more efficient filing area and a break/lunch area.

Project Limits: Prosecutor's office space on the second floor of the Stubbs Justice Center.

The project advertising and bidding will be done through the Purchasing Dept. by the Prosecutor's Office per Williams Marras.

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	10/8/2007	11/2/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Rack 29 Emergency Repair	2007-001-00	

Description

Project Objective: Repair the overflow line at Rack 29. The headwall and 120 feet of brick sewer have washed away. The sewer runs through an old sanitary landfill.

Project Limits: Rack 29

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Construction Phase	1/18/2007	4/24/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Romig Road Median - Emerg	2007-084-00	

Description

Project Objective: To remove the existing concrete median and the existing tree medians and replace these areas with concrete pavement. This will make the businesses more accessible and improve the access for semi truck deliveries to businesses. Contractor is Vito Gironda Construction Co.

Project Limits: From Vernon Odom Blvd to just north of Kendale Dr.

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Construction Phase	10/22/2007	11/16/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
S. Broadway Street Traffic Signal	2007-006-00	

Description

Project Objective: Relocate the existing traffic signal at the Summit County Courthouse to better align with its main entrance.

Project Limits: S. Broadway Street near the Summit County Courthouse

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	2/27/2007	4/20/2007
Construction Phase	10/15/2007	11/13/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
S. Broadway Street Traffic Signal	2007-006-00	

Description

Project Objective: Relocate the existing traffic signal at the Summit County Courthouse to better align with its main entrance.
Project Limits: S. Broadway Street near the Summit County Courthouse

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	2/27/2007	4/20/2007
Construction Phase	10/15/2007	11/13/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
S. Main St. Bridges over I-277	2003-039-00	

Description

Project Objective: ODOT will re-deck and paint one structure under S. Main Street at I-277.
Project Limits: N/A

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Construction Phase	2/5/2007	11/1/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Sanitary Sewer Reconstruction 2005 RECORD DRAWINGS	2004-043-00	

Description

Project Objective: To reconstruct existing broken or damaged sanitary sewers and to reconstruct or construct sanitary manholes.

Project Limits: 1. Yorkshire Drive ~ 303' from Vicgross to the east
2. Tonawanda Avenue ~ 367' from Newton to the south
3. Park Street ~ 673' from first manhole west of Forge to Union
4. Harrison Avenue & 6th Street ~ add three manholes to turn the flows from the north and the south to the west

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Construction Phase	1/24/2007	5/11/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Sanitary Sewer Reconstruction 2008	2007-027-00	

Description

Project Objective: To repair existing broken or damaged sanitary sewers by reconstruction and lining, and to reconstruct or construct sanitary manholes. Relocate/reconstruct the existing 12" sanitary sewer and the 39" storm sewer that currently is located within an easement that runs through the property bounded by E. Miller Avenue to the south and Bellows Street to the east. These sewers will be relocated to the Bellows and E. Miller. There is approximately 920 lf of 12" sanitary and 935 lf of storm. Approximately, 660 lf each of 12" sanitary and 39" storm sewers that will be abandoned in place within the easement.

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	2/26/2007	4/11/2008

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Sherwood Dr Retaining Wall Emerg	2007-065-00	

Description

Project Objective: Rebuild a failed retaining wall that is retaining Sherwood Dr. The contractor is Kenmore Construction.
Project Limits: Sherwood Dr. - 300' north of Morningside

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	4/1/2007	6/30/2007
Construction Phase	10/1/2007	11/30/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Sherwood Dr Retaining Wall Emerg	2007-065-00	

Description

Project Objective: Rebuild a failed retaining wall that is retaining Sherwood Dr. The contractor is Kenmore Construction.
Project Limits: Sherwood Dr. - 300' north of Morningside

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	4/1/2007	6/30/2007
Construction Phase	10/1/2007	11/30/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Smith Ghent Slope Stabilization	2003-060-00	

Description

Project Objective: Repair deteriorating slopes on the existing detention basin
Project Limits: Smith Road at Ghent Road (Sterling Complex)

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	6/25/2007	10/8/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
South Main Street Parking RECORD DRAWINGS	2007-011-00	

Description

Project Objective: Design and construct 3 parking lots to service 1115 South Main Street.
Project Limits: 1115 South Main Street

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	1/31/2007	12/26/2007
Construction Phase	6/21/2007	10/26/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
South Main Street Parking RECORD DRAWINGS	2007-011-00	

Description

Project Objective: Design and construct 3 parking lots to service 1115 South Main Street.
Project Limits: 1115 South Main Street

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	1/31/2007	12/26/2007
Construction Phase	6/21/2007	10/26/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Spicer St. & Gray Ct. Roadway Improvements	2006-005-00	

Description

Project Objective: To improve Spicer Street & Gray Court by reconstructing the pavement, sidewalk, curb & gutter, and storm sewer as necessary.
Project Limits: Spicer Street (Power Street to E. Exchange Street) & Gray Court (Spicer Street to Emmitt Court)

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	6/25/2007	1/23/2008

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Spicertown Public Parking RECORD DRAWINGS	2006-001-00	

Description

Project Objective: A parking lot is proposed for the southwest corner of Abbott Court and Spicer Street. The proposed parking lot will have approximately 23 parking spaces.
Project Limits: Parcels currently addressed as 396, 400 and 406 Spicer Street.

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Construction Phase	7/16/2007	10/19/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Stan Hywet Trail Improv. Proj. B	2006-063-01	

Description

Project Objective: Drystone retaining wall reconstruction.
Project Limits: Stan Hywet property.

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Construction Phase	7/9/2007	8/2/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Street Tree Replacement 2007	2007-002-00	

Description

Project Objective: Annual replacement of trees removed due to age, disease or accidents.
Project Limits: City wide

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	1/11/2007	1/11/2007
Construction Phase	3/29/2007	5/4/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Street Tree Replacement 2007	2007-002-00	

Description

Project Objective: Annual replacement of trees removed due to age, disease or accidents.
Project Limits: City wide

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	1/11/2007	1/11/2007
Construction Phase	3/29/2007	5/4/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Stubbs Justice Center ADA Restrooms	2007-040-00	

Description

Project Objective: Renovate one set of men's and women's restrooms on the fourth and eighth floors to ADA standards.
Project Limits: The H. K. Stubbs Justice Center

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	3/19/2007	5/18/2007
Construction Phase	10/22/2007	1/11/2008

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Stubbs Justice Center ADA Restrooms	2007-040-00	

Description

Project Objective: Renovate one set of men's and women's restrooms on the fourth and eighth floors to ADA standards.
Project Limits: The H. K. Stubbs Justice Center

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	3/19/2007	5/18/2007
Construction Phase	10/22/2007	1/11/2008

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Stubbs Justice Center Fire Alarm	2006-036-00	

Description

Project Objective: Modernize the Justice Center fire alarm system.
Location: The H. K. Stubbs Justice Center

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Construction Phase	2/26/2007	6/15/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Stubbs Justice Center HVAC Record Drawing	2006-021-00	

Description

Project Objective: Modernize the building HVAC system by replacing the major air conditioning components and by replacing individual HVAC units in court room suites on floors 8 & 9 and the Chief's offices on floor 3.

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Construction Phase	1/15/2007	6/1/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Stubbs Justice Center Vestibule	2007-054-00	

Description

Project Objective: Provide improved ingress and egress control and lobby security for the H. K. Stubbs Justice center.
Project Limits: The H. K. Stubbs Justice Center and immediate site.

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	9/24/2007	10/5/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Stubbs Property Room Expansion	2006-041-00	

Description

Project Objective: Expand the Police Property Room to provide improved security and additional administrative space.
Project Limits: The Stubbs Police Property Room and Building Maintenance offices.

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Construction Phase	1/29/2007	2/27/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Summit Lake Maintenance Building RECORD DRAWINGS	2007-012-00	

Description

Project Objective: Construct a new 16'X20' maintenance building including water and electric.
Project Limits: Summit Lake Community Center grounds

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	3/12/2007	3/12/2007
Construction Phase	7/30/2007	11/2/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Summit Lake Maintenance Building RECORD DRAWINGS	2007-012-00	

Description

Project Objective: Construct a new 16'X20' maintenance building including water and electric.
Project Limits: Summit Lake Community Center grounds

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	3/12/2007	3/12/2007
Construction Phase	7/30/2007	11/2/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Superblock Deck Utility Relocation	2007-003-02	

Description

Project Objective: Relocate existing utilities in Dart Avenue in order to construct the Superblock Deck Expansion
Project Limits: Dart Avenue (W. Mill St. to Ramp C/F Innerbelt)
Project is cancelled per Ken Kostura on 12/27/2007

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	9/19/2007	1/24/2008

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Superblock Elevators & Lobbies	2007-069-00	

Description

Project Objective: Replace 3 existing elevators, add 1 new elevator, rehab existing elevator lobbies and stairwells
Project Limits: Superblock Parking Deck

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	9/19/2007	10/26/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Superblock Parking Deck 2007	2007-004-00	

Description

Project Objective: To design and construct improvements to lighting, signage, parking control equipment, and elevators
Project Limits: Superblock Parking Deck

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	2/15/2007	9/21/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Superblock Pkg Deck West Expansion	2007-003-00	

Description

Project Objective: Expansion of the existing Superblock Parking Deck to the west over Dart Avenue.
Project Limits: East of Dart Ave., north of Superblock Parking Deck

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	2/15/2007	11/16/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Thayer Street Record Drawing	2005-004-00	

Description

Project Objective: To reconstruct existing street
Project Limits: From Tallmadge Avenue to Cuyahoga Falls Avenue

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Construction Phase	5/29/2007	9/14/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Tot Lot Rehabilitation 2006	2006-039-00	

Description

Project Objective: Install new play equipment at Ed Davis Community Center
Project Limits: Ed Davis Community Center

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Construction Phase	4/27/2007	6/8/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Tot Lot Rehabilitation 2007	2007-045-00	

Description

Project Objective: Install new play equipment at Summit Lake Community Center
Project Limits: Summit Lake Community Center

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	4/2/2007	5/18/2007
Construction Phase	10/15/2007	11/9/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Tot Lot Rehabilitation 2007	2007-045-00	

Description

Project Objective: Install new play equipment at Summit Lake Community Center
Project Limits: Summit Lake Community Center

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	4/2/2007	5/18/2007
Construction Phase	10/15/2007	11/9/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
W. Market St. Utility Reconnection SUM - 18-5.99 Record Drawings	2006-026-00	

Description

Project Objective: To relocate ocerhead utilities underground in anticipation of the future roadway project.
Project Limits: Waldorf Drive to Ohio Edison Drive

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Construction Phase	2/19/2007	9/7/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Waterloo Rd. Towpath Underpass	2004-040-00	

Description

Project Objective: For Summit County to construct an underpass for the towpath trail under Waterloo Rd. (The City of Akron will be a financial partner).
Project Limits: Waterloo Road Bridge over Canal

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Construction Phase	5/7/2007	11/30/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Waters Park Shuffle Board Canopies	2007-044-00	

Description

Project Objective: Refurbish the canopy structure and replace the canvas on two canopies. Also reroof the concession / restroom building.
Project Limits: The shuffle board canopies and concession / restroom building at Waters Park.
Note: This project was performed under a purchase order by South Akron Awning Company under P.O. P0702953.

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	4/2/2007	4/20/2007
Construction Phase	5/1/2007	5/30/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Waters Park Shuffle Board Canopies	2007-044-00	

Description

Project Objective: Refurbish the canopy structure and replace the canvas on two canopies. Also reroof the concession / restroom building.
Project Limits: The shuffle board canopies and concession / restroom building at Waters Park.
Note: This project was performed under a purchase order by South Akron Awning Company under P.O. P0702953.

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	4/2/2007	4/20/2007
Construction Phase	5/1/2007	5/30/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
West Market St. Sum-18-5.99	2002-105-00	

<i>Description</i>
Roadway Improvements Project Limits: Pershing Avenue to Hawkins Avenue

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Construction Phase	6/11/2007	

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
West Side Office Park Phase 2	2006-064-00	

<i>Description</i>
Project Objective: To secure a grant from the State of Ohio to build an infrastruce for a new office park. Project Limits: Zazo and Hanson Properties off of White Pond Drive

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	4/23/2007	8/27/2007

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
White Pond Drive Phase 1	2004-029-00	

<i>Description</i>
Project Objective: Widen and reconstruct pavement, install storm and sanitary sewer as required, upgrade water main and street lighting. Project Limits: 500'± north at Mull Ave. to Wheeling & Lake Erie Railroad.

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Construction Phase	11/26/2007	8/15/2008

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Whitestone Avenue	2007-008-00	

<i>Description</i>
Project Objective: Reconstruct pavement within access drive limits for Family Dollar Store (1156 East Tallmadge Avenue) on Whitestone Avenue. This work incudes pavement, curbing, drive apron reconstruction, lawn restoration and incidental items. Project Limits: Whitestone Avenue - Start approximately 75 feet south of south Right of Way of Tallmadge Avenue for a length of 125 LF

<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Design Phase	1/29/2007	9/23/2009

<i>Project Name</i>	<i>AebProjectID</i>	<i>File No.</i>
Yukon Avenue Improvement	2006-048-00	
<i>Description</i>		
Project Objective: Construct full improvements to extend Yukon Avenue. Project Limits: Thurston to Slosson Note: The developer is Shalmo Builders, Inc., 464 Etheridge Blvd., Canal Fulton, OH 44614		
<i>Activity Description</i>	<i>Activity Start</i>	<i>Activity Finish</i>
Construction Phase	7/2/2007	4/27/2008
